



Inverness West Link Stage 2



Community Liaison Meeting
24th February 2020

Steve Scott





Project Update –

- Earthworks @ 95% complete
- Drainage and services @ 90% complete
- Streetlighting @ 90% complete
- Kerbing and lock block @ 90%
- Surfacing @ 50% complete
- Sheet Piling 100% complete
- Concrete Anchor Wall 100%
- Welding to piles 90%
- Concrete Capping beams 55%
- Ducts under canal and Concrete Invert 100%
- A82 Diversion



Project Update – Piling & Dewatered Canal





Project Update – Piling & Dewatered Canal





Project Update – Electrofishing in the canal



2000 fish recovered
and relocated from
the canal. Lamprey,
trout and eels





Project Update – Concrete Anchor Wall






Project Update – Footpath, kerbs, surfacing and street lighting on GBR





Project Update – Traffic Management on A82 / GBR

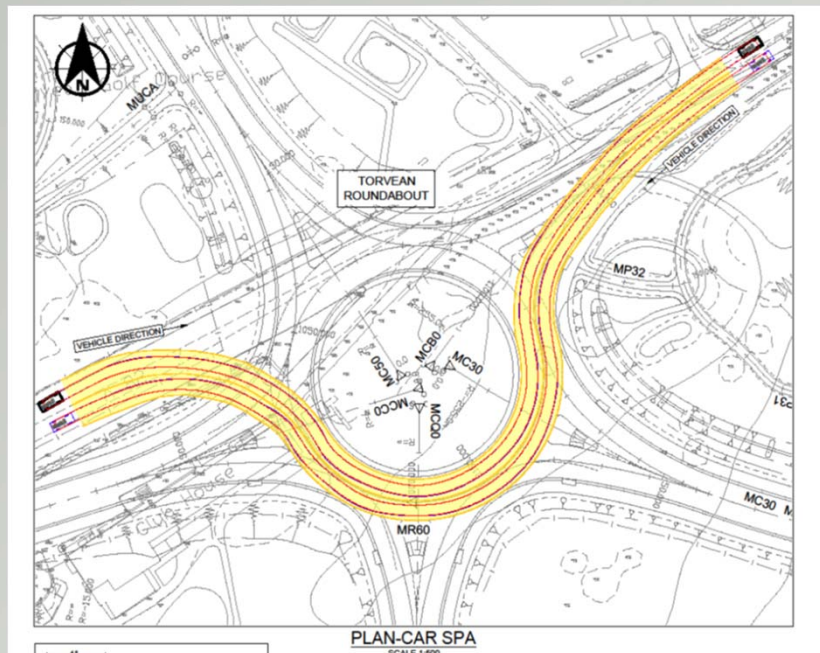

- Overnight closure on A82 10th February to allow surfacing and white lining.
- Overnight closures on A82 w/c 9th March for 4 nights for bridge controls
- Planned closure on General Booth Road 16th March for 3 weeks due to condition of existing road
- Future closures on A82 for surface tie ins



Project Update – A82 Diversion





Community Benefit – Local groups, schools and charities

- Open Meeting on site on the 12th September
- Cycling Without Age / Spokes for Folks
- Sponsored Inverness Rowing Club Head Regatta
- Assist Inverness Rowing Club with development plans
- Sponsoring Maps for a local Orienteering Event
- Highland Schools Hockey - Medals
- Park Run - Markers
- Charleston Academy Maths Department visit
- Glen Urquhart High School – Talk on role of Civil Engineers and the Project to S5
- Visit from Scottish Canals – Youth Group and Lock Keepers
- UHI Visits – Engineering and Quantity Surveying
- Kinmylies Primary - Talk on Civil Engineers and the Project to all pupils, dropped off a time capsule to be filled by pupils and installed in the bridge wall
- Bridges for Schools Initiative
- STEM Ambassadors
- ICE Visit
- Press Visit





Planned Works

- Surfacing – General Booth Road & roundabout and footpaths
- Concrete Capping Beams and bridge slabs
- Concrete Invert to canal and slope protection works
- Timber Jetty
- Remove all propping and falsework
- Remove pumps and pipelines
- Remove dams
- Canal open for Monday 23rd March
- Underpass installation
- Bridge fabrication due to commence this week
- Bridge due to be delivered in 6 sections mid July and welded together on site



Progress Photo – New Wharf





Progress Photo – Canal Works





Progress Photo





Progress Photo





CAPITA

Questions ?



WEST LINK Connecting our communities
A' ceangal ar coimhearsnachdan

