



# Caol & Lochyside Flood Prevention Scheme



Community Liaison Meeting  
23<sup>rd</sup> June 2021



Project Manager : Steve Scott BEng CEng MICE



## Project Update –


### Phase 1

- Turf Cutting Ceremony
- Site Compound established and satellite facilities at the Shinty clubhouse
- Access and storage area at Caol spit
- Welding of water pipe for new service to replace main under embankment
- Installation of septic tank at Shinty clubhouse
- Japanese Knotweed removal along shore
- Commenced removal of 900mm dia raw water pipe on shore
- Tree pruning and strimming along shinty access road
- Letter drop to residents



## Project Phasing – Erracht Drive Phase 1 ( June – September 21 )

Erracht Drive - Phase 1 – Site Establishment, clearance and drainage outfalls



Activity	Key	Mitigation
Compound and Site Establishment		Dedicated access points, one way system on Erracht Drive in operation
Service diversions		Signal Controlled single lane working (where required)
Japanese knotweed removal		Works contained within site. Refinement of material on site reducing vehicle required for disposal
Drainage outfall installation		Works contained within site. Use of precast headwall where possible to minimise material deliveries
Site Access Points		Designated access points to control traffic movements. Use of one way system along Erracht Drive
Site Access Route		Access route with site boundary minimising traffic on Erracht Drive

### Project Mitigation Measures

- Use of vehicular one way system eastward for site traffic along Erracht Drive shore front to site compound.
- Access to Site compound.
- Site construction extends from southern kerb of Erracht Drive for majority of works maintaining unrestricted traffic flow for as much of the project as possible
- Pedestrian access maintained along north footway of Erracht Drive
- Designated crossing points where cycle routes, footways, Great Glen way cross the works with Access maintained throughout.
- Footway at base of canal and towpath maintained throughout with localised diversion during direct tie in works
- Internal site track along frontage providing site access and removing traffic from public road
- Dedicated site access points ensuring safe access and egress
- Access maintained to canal parks, shinty club and residential properties.
- Public and businesses kept up to date with liaison groups and notice boards.





## Progress Photos - Turf Cutting Ceremony – 1<sup>st</sup> June 2021





## Progress Photos - Removal of Raw Water Pipe





## Progress Photos - Welding of Water Main





## Progress Photos - Aerial Photo from the Caol Spit





## Progress Photos - Aerial Photo of topsoil strip at shinty club







## Planned Works for next 4 weeks

- Continue with removal of Raw Water pipe
- Service diversions
- Take delivery of drainage materials
- Make site safe for 2 week trade shutdown ( 24<sup>th</sup> July to 8<sup>th</sup> August )




## Community Benefit - Update

- Employed 1 local cleaner and 2 local labourers
- Small workforce who stay in the Lochaber area
- Contracting with local firms and supply chain
- Engagement with schools and colleges regarding site visits, presentations, training, work experience and placements
- Engaging with the job centre regarding future positions




# Traffic Management – Kilmallie Road

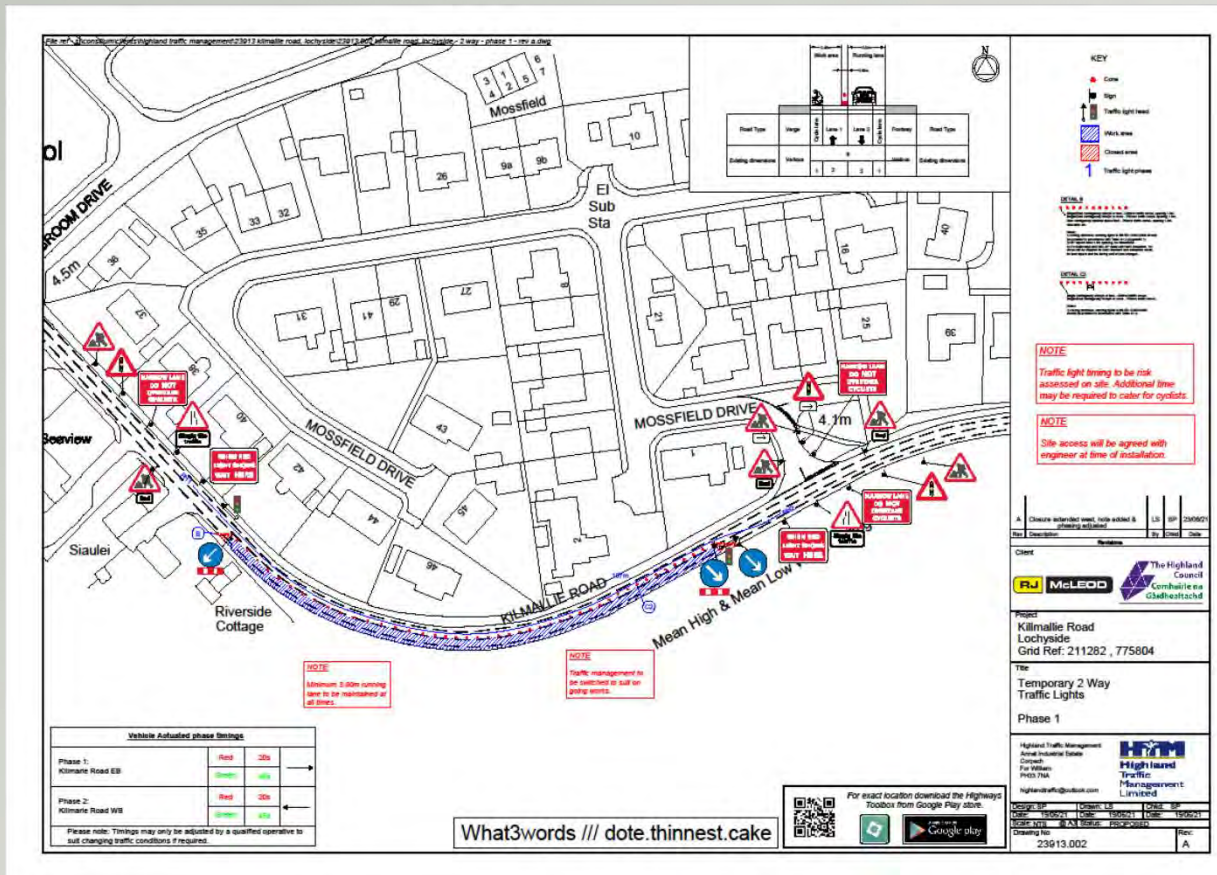




## Traffic Management – Erracht Drive

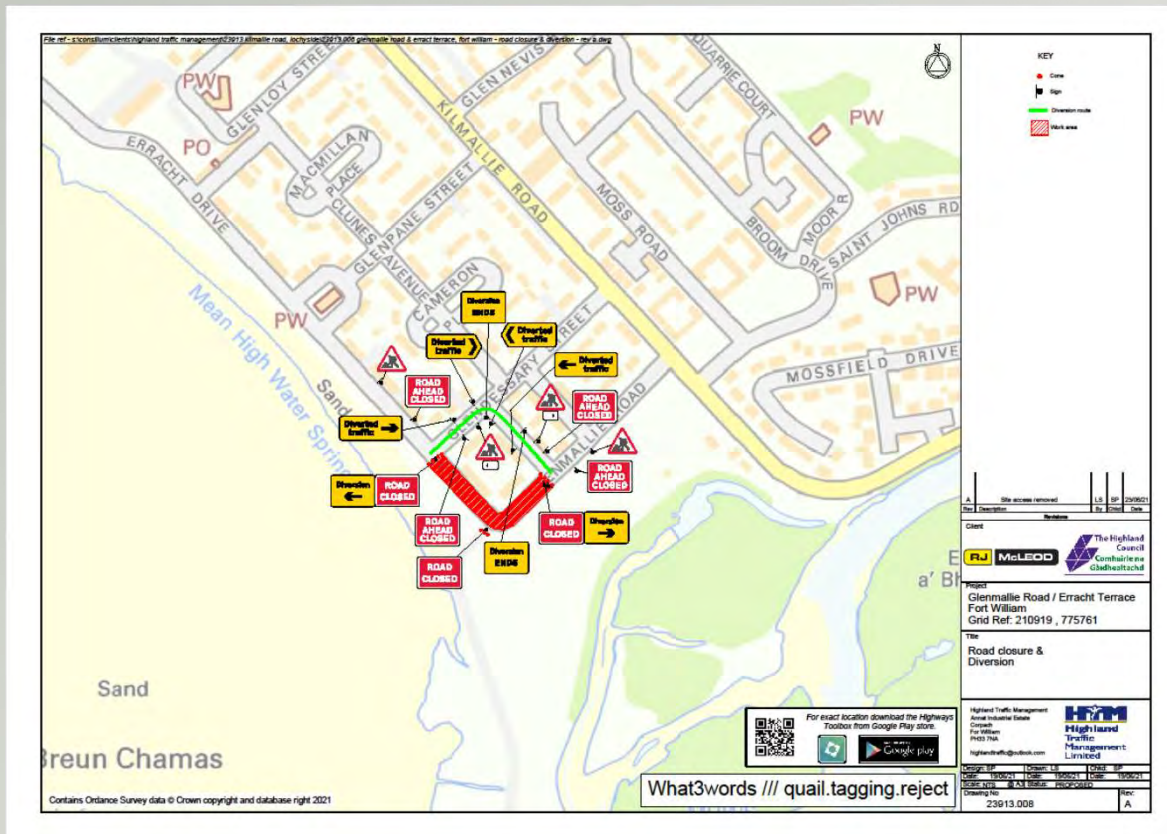



## Traffic Management – Site Access off A830

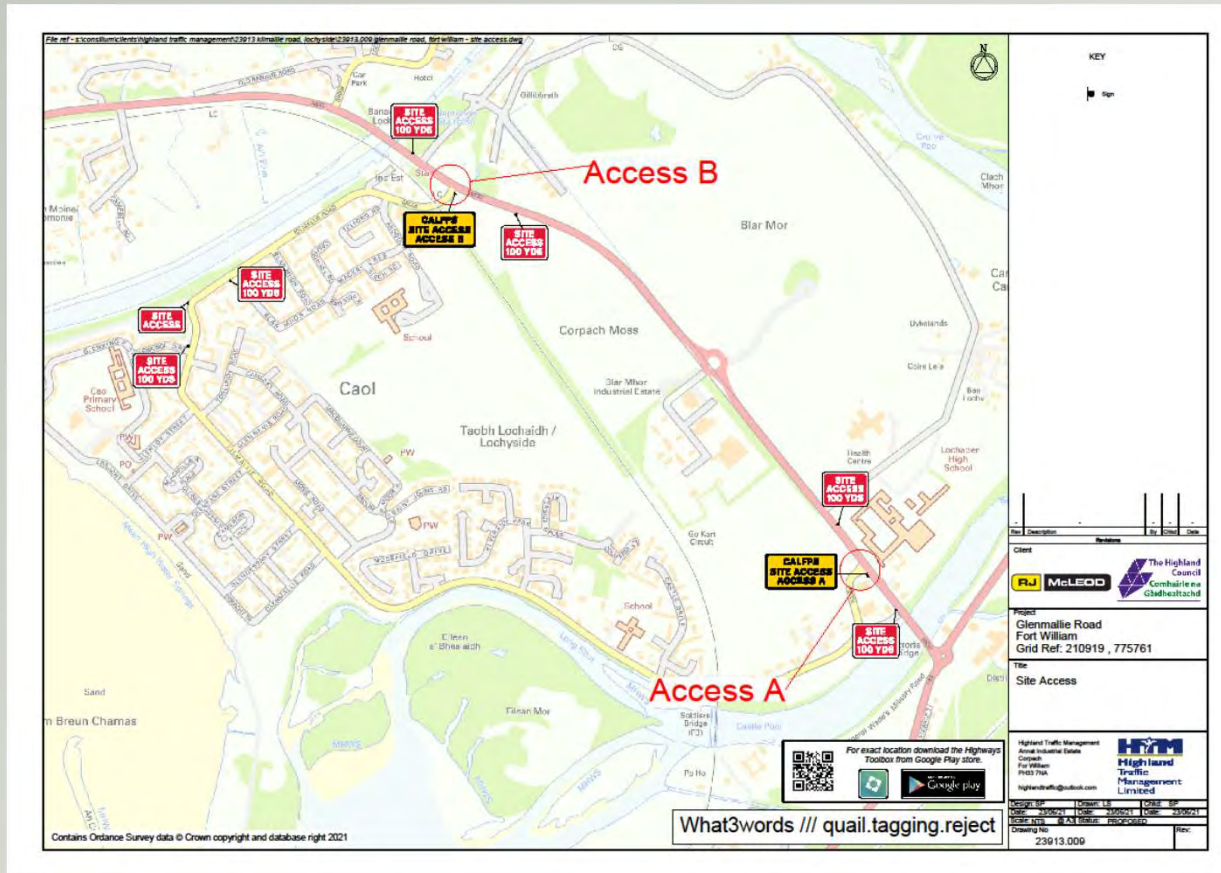



**Any Questions?**
