



Caol & Lochyside Flood Protection Scheme



Community Liaison Meeting
25th July 2023





Project Update –

Kilmallie Rd flood wall

- Gully installation on Kilmallie road has been completed but TM remains split into 2 sections of for other activities until the end of the week
- 11KV Cable diversion Complete
- Riverside erosion control and reinstatement works will be ongoing.
- Replacing damaged kerbs & upfilling/Soiling from kerb to wall face ongoing

Caol foreshore flood embankment.

- Rock armour works to Caol spit are 99% complete.
- Croft access on embankment has been completed
- Remaining material from Shinty club compound removed
- Community Shed Installed, meter installation set at 25/08/23 Sparky's installing equipment the following day
- Gabion mattress construction adjacent to Caol spit access complete.



Kilmallie Rd – Traffic management phasing





Caol foreshore – Fill material delivery route






Progress Photos Foreshore





Progress Photos – Foreshore

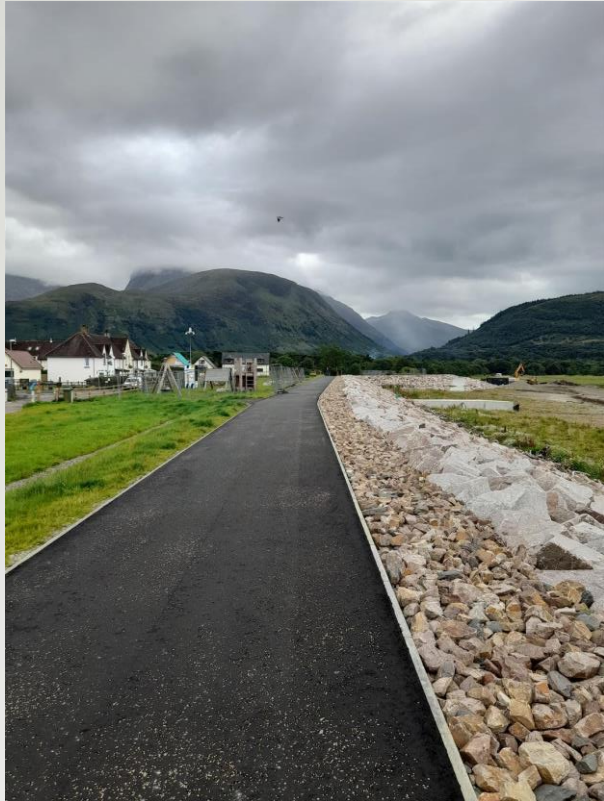



Progress Photos – Foreshore





Progress Photos – Foreshore





Progress Photos – Kilmallie Road





Progress Photos – Kilmallie Road





Planned Works for next period up to end of August.

Kilmallie Rd flood wall

- Riverside erosion control and reinstatement works will be ongoing.
- 9Nr Gully lid replacement @ site entrance.
- HSC on site W/C 07/08/23 & w/c 14/08/23 – Plane & Surdace Kilmallie Rd
- Reinststate area @ Wet well
- Construct Grasscrete area @ Wet well
- Construct new planter @ Wet well
- Road Signage install



Planned Works for next period up to end of August

Caol foreshore flood embankment

- HSC on site W/C 07/08/23 & w/c 14/08/23 – to Plane/surface Kilmallie Rd & Surface Turning head + Footpath @ Shinty Club
- Rock armour works to Caol spit will be finished following removal of excess material.
- Landscaping (De-stoning & Seeding)
- Install Fridge + Freezer until meter installation date
- Fencing around Caol Spit & Kilmallie Rd
- Play park inspection complete
- Signage install



Community Benefits

- **90% of site personnel reside in the Highlands.**
- **65% of site personnel live within 75-mile radius of the site.**
- **50% of site personnel are locals (live within a 10-mile radius of the site).**
- **To date we have employed 2 local labourers, 1 ganger, 2 machine operators and 4 local cleaners all living within 2 miles of the site.**
- **Adverts in job centre for labourers and machine operators.**
- **Discussions with the local schools on talks, time capsules and training for secondary pupils. We currently have a work experience pupil on site.**
- **Donation of shinty equipment to Lochaber High School.**
- **An alternative design proposal for part of the works has generated benefits including reduced vehicle movements and a financial saving which is allocated to be spent on Community Benefits.**



Community Field – following excavator levelling works





AOB

Any Questions?
