



Uig Harbour Redevelopment



Community Liaison Meeting
20th January 2022



Project Manager : Steve Scott BEng CEng MICE




Project Involvement

- **Client : The Highland Council**
- **Funder : Transport Scotland**
- **Asset owner for Ferries and Existing Terminal Building : Caledonian Maritime Assets Ltd (CMAL)**
- **Ferry Operator : Caledonian MacBrayne Ferries Ltd (CFL)**
- **Client Consultant : AECOM Ltd**
- **Contractor : RJ McLeod (Contractors) Ltd**
- **Contractor Consultant : Wallace Stone**



Existing Pier

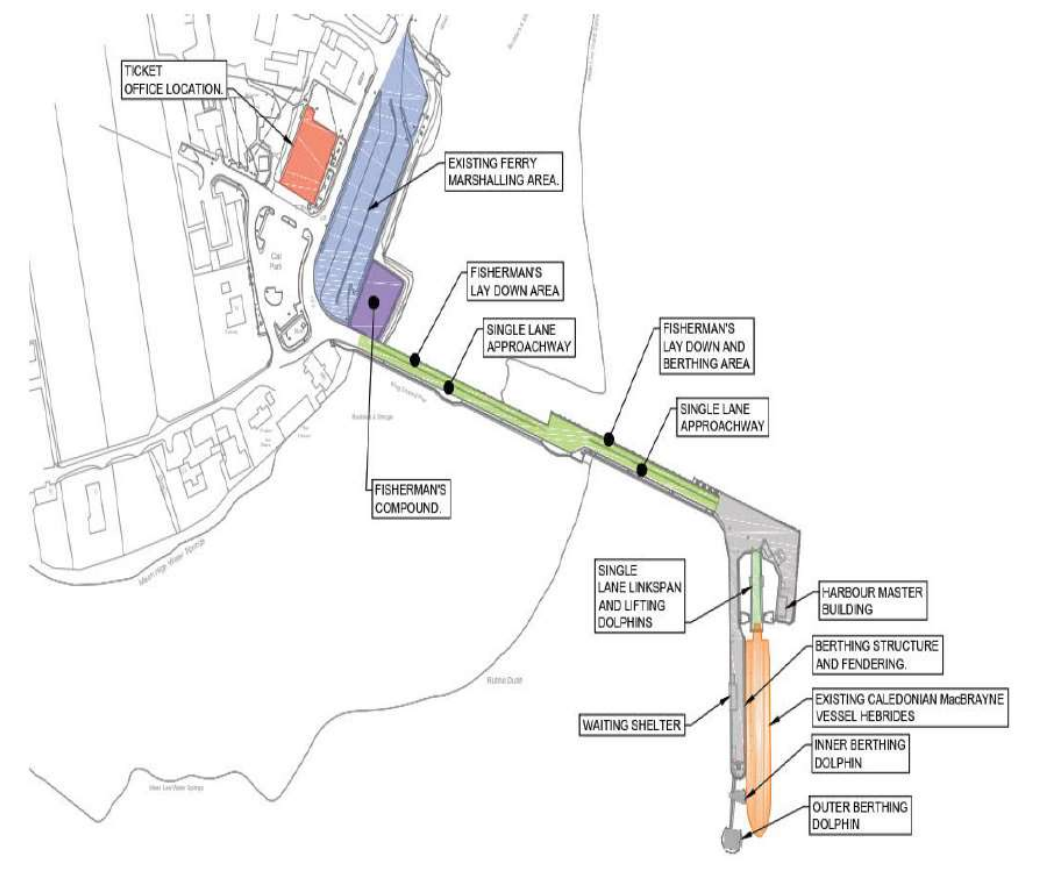




Project Summary

- **Foreshore reclamation to provide a larger marshalling, parking and storage area**
- **New Terminal Building (by others)**
- **6 metre widening of approach structures**
- **New 16m wide breakwater structure and waiting room**
- **Demolition of existing and installation of new dolphins, bankseat and Linkspan**
- **New fenderline piles, fender units and pier furniture**
- **Extensive concrete repairs**
- **Dredging**
- **LNG Infrastructure**



Project Plan

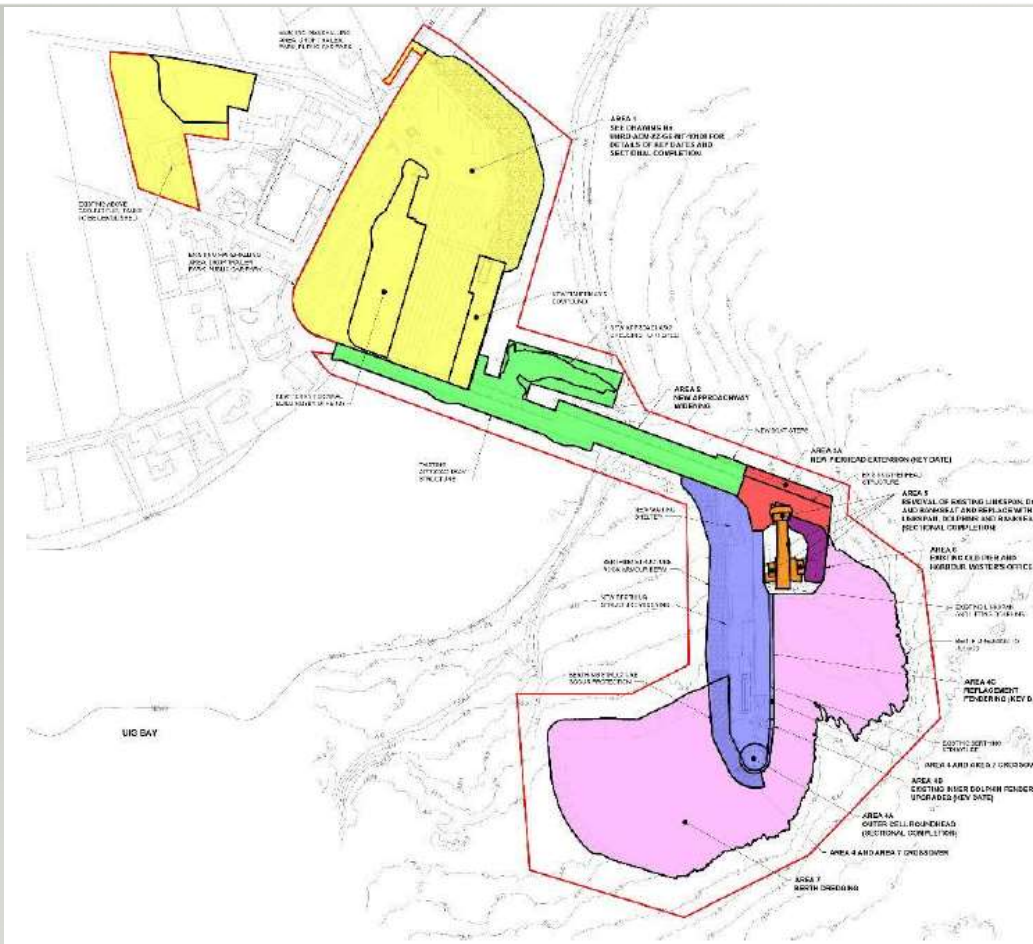



Project – Materials

- **Fill Material – 130,000 tonnes**
- **Armour Material – 20,000 tonnes**
- **Concrete – 13,000 tonnes**
- **Steel Reinforcing – 1000 tonne**
- **Sheet Piles – 2,800 tonnes**
- **Drainage Pipes & Precast – 1000 tonnes**
- **Dredging – 30,000m³**

Taking into consideration plant movements, fuel and incidental deliveries there will be over 15,000 HGV movements to the site.



Project – Programme

- **2 year Programme**
- **Reclamation area due to start imminently**
- **Piling start spring / summer 2022 – Spring 2023**
- **Outage Planned for 22nd Sept 2022 – 3rd Feb 2023**
- **Dolphins, Bankseat and Linkspan installed during outage period**



Public Liaison

- **Press Releases at key stages of the project**
- **Monthly updates on progress and planned works on Highland Council Website, Community facebook and Community noticeboards**
- **CLG meetings with presentation on progress**
- **Liaison with stakeholders**
- **Project information board**



Community Benefit

- **Supplemented with employment of local personnel**
- **Contracting with local firms and supply chain**
- **Engagement with schools and colleges regarding site visits, presentations, training, work experience and placements**
- **Engaging with the job centre regarding future positions**



Planned Works for next 4 weeks

- **Complete Site Establishment**
- **Commence works on filling to the reclamation area**
- **Commence Concrete Repairs**
- **Heras Fencing to work areas**
- **Site Clearance**
- **Temporary Moorings**
- **Design Work**



Uig Harbour Redevelopment – Any Questions?

