

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor:	Resource Names	Critical	3rd Quarter			4th Quarter			1st Quarter			2nd Quarter	
									May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
1		THC Integrated transition & Transformation Plan	870 days?	Aug 1 '16	Dec 1 '19			Yes											
2		MS: Fujitsu Exit to Transition	0 days	Oct 1 '16	Oct 1 '16			No											
3		MS :Contract Sign off	1 day	Sep 6 '16	Sep 6 '16	34		Yes											
4		MS:Agreed Implementation Plan	0 days	Oct 4 '16	Oct 4 '16	75		No											
5		MS: Network Migration Link Commissioning	0 days	Nov 16 '16	Nov 16 '16	43		No											
6		MS: Service Desk, DC Infrastructure and tools Setup Complete	0 days	Dec 12 '16	Dec 12 '16	251		No											
7		MS: Tranche 1 ATP Services Go Live (SD, EUC, App Ops)	0 days	Feb 17 '17	Feb 17 '17	108,158,13		No											
8		MS: Tranche 2 ATP Services Go Live (DC Support)	0 days	Mar 10 '17	Mar 10 '17	162		No											
9		MS:CPP Services Stabilized	0 days	May 1 '17	May 1 '17	8		No											
10		MS ATP :Transformation Project 1- Active Directory (including processes for joiners/movers/leavers)	0 days	Feb 9 '17	Feb 9 '17	299		No											
11		MS CPP Transformation Project 1- Active Directory (including processes for joiners/movers/leavers)	0 days	Mar 1 '17	Mar 1 '17	10		No											
12		MS ATP Transformation Project 2 - Data Centre Transformation	0 days	Mar 10 '17	Mar 10 '17	275		No											
13		MS Transformation Project 2 - DC Setup Complete and Microsoft Office Milestone	0 days	Dec 13 '16	Dec 13 '16	245		No											
14		MS CPP Transformation Project 2 - Data Centre Transformation	0 days	Apr 1 '17	Apr 1 '17	12		No											
15		MS Key Core Services Transition Completed and Transformation Projects 1, 2 & 6 Complete	0 days	Apr 1 '17	Apr 1 '17	14		No											
16		MS CPP Transformation Project Office Replacement Service	0 days	Jun 6 '17	Jun 6 '17	307		No											
17		MS ATP Transformation Project 3 - Corporate Desktop Refresh	0 days	May 1 '17	May 1 '17	339		No											
18		MS Key Transformation Project 3 – Corporate Desktop Refresh	0 days	Sep 1 '17	Sep 1 '17	17		No											
19		MS CPP Transformation Project 3 - Corporate Desktop Refresh	0 days	Nov 15 '17	Nov 15 '17	340		No											
20		MS ATP Transformation Project 4 - Curriculum Desktop Refresh	0 days	May 15 '17	May 15 '17	345		No											
21		MS Key (50%) Transformation Project 4 – Curriculum refresh	0 days	Aug 31 '18	Aug 31 '18			No											
22		MS CPP Transformation Project 4 - Curriculum Desktop Refresh	0 days	Nov 15 '19	Nov 15 '19	346		No											
23		MS ATP LMD - Deployment and final removal of devices	0 days	Aug 16 '19	Aug 16 '19	347		No											
24		MS Transformation Project 3 and 4 – Desktop Environment Setup Complete	0 days	Nov 15 '19	Nov 15 '19	336,346		No											
25		MS CPP Transformation Project 5 – Business Application transformation	1 day	Feb 16 '17	Feb 16 '17	384		No											


Project: Detail Implementation
Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			




Project: Detail Implementation
 Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

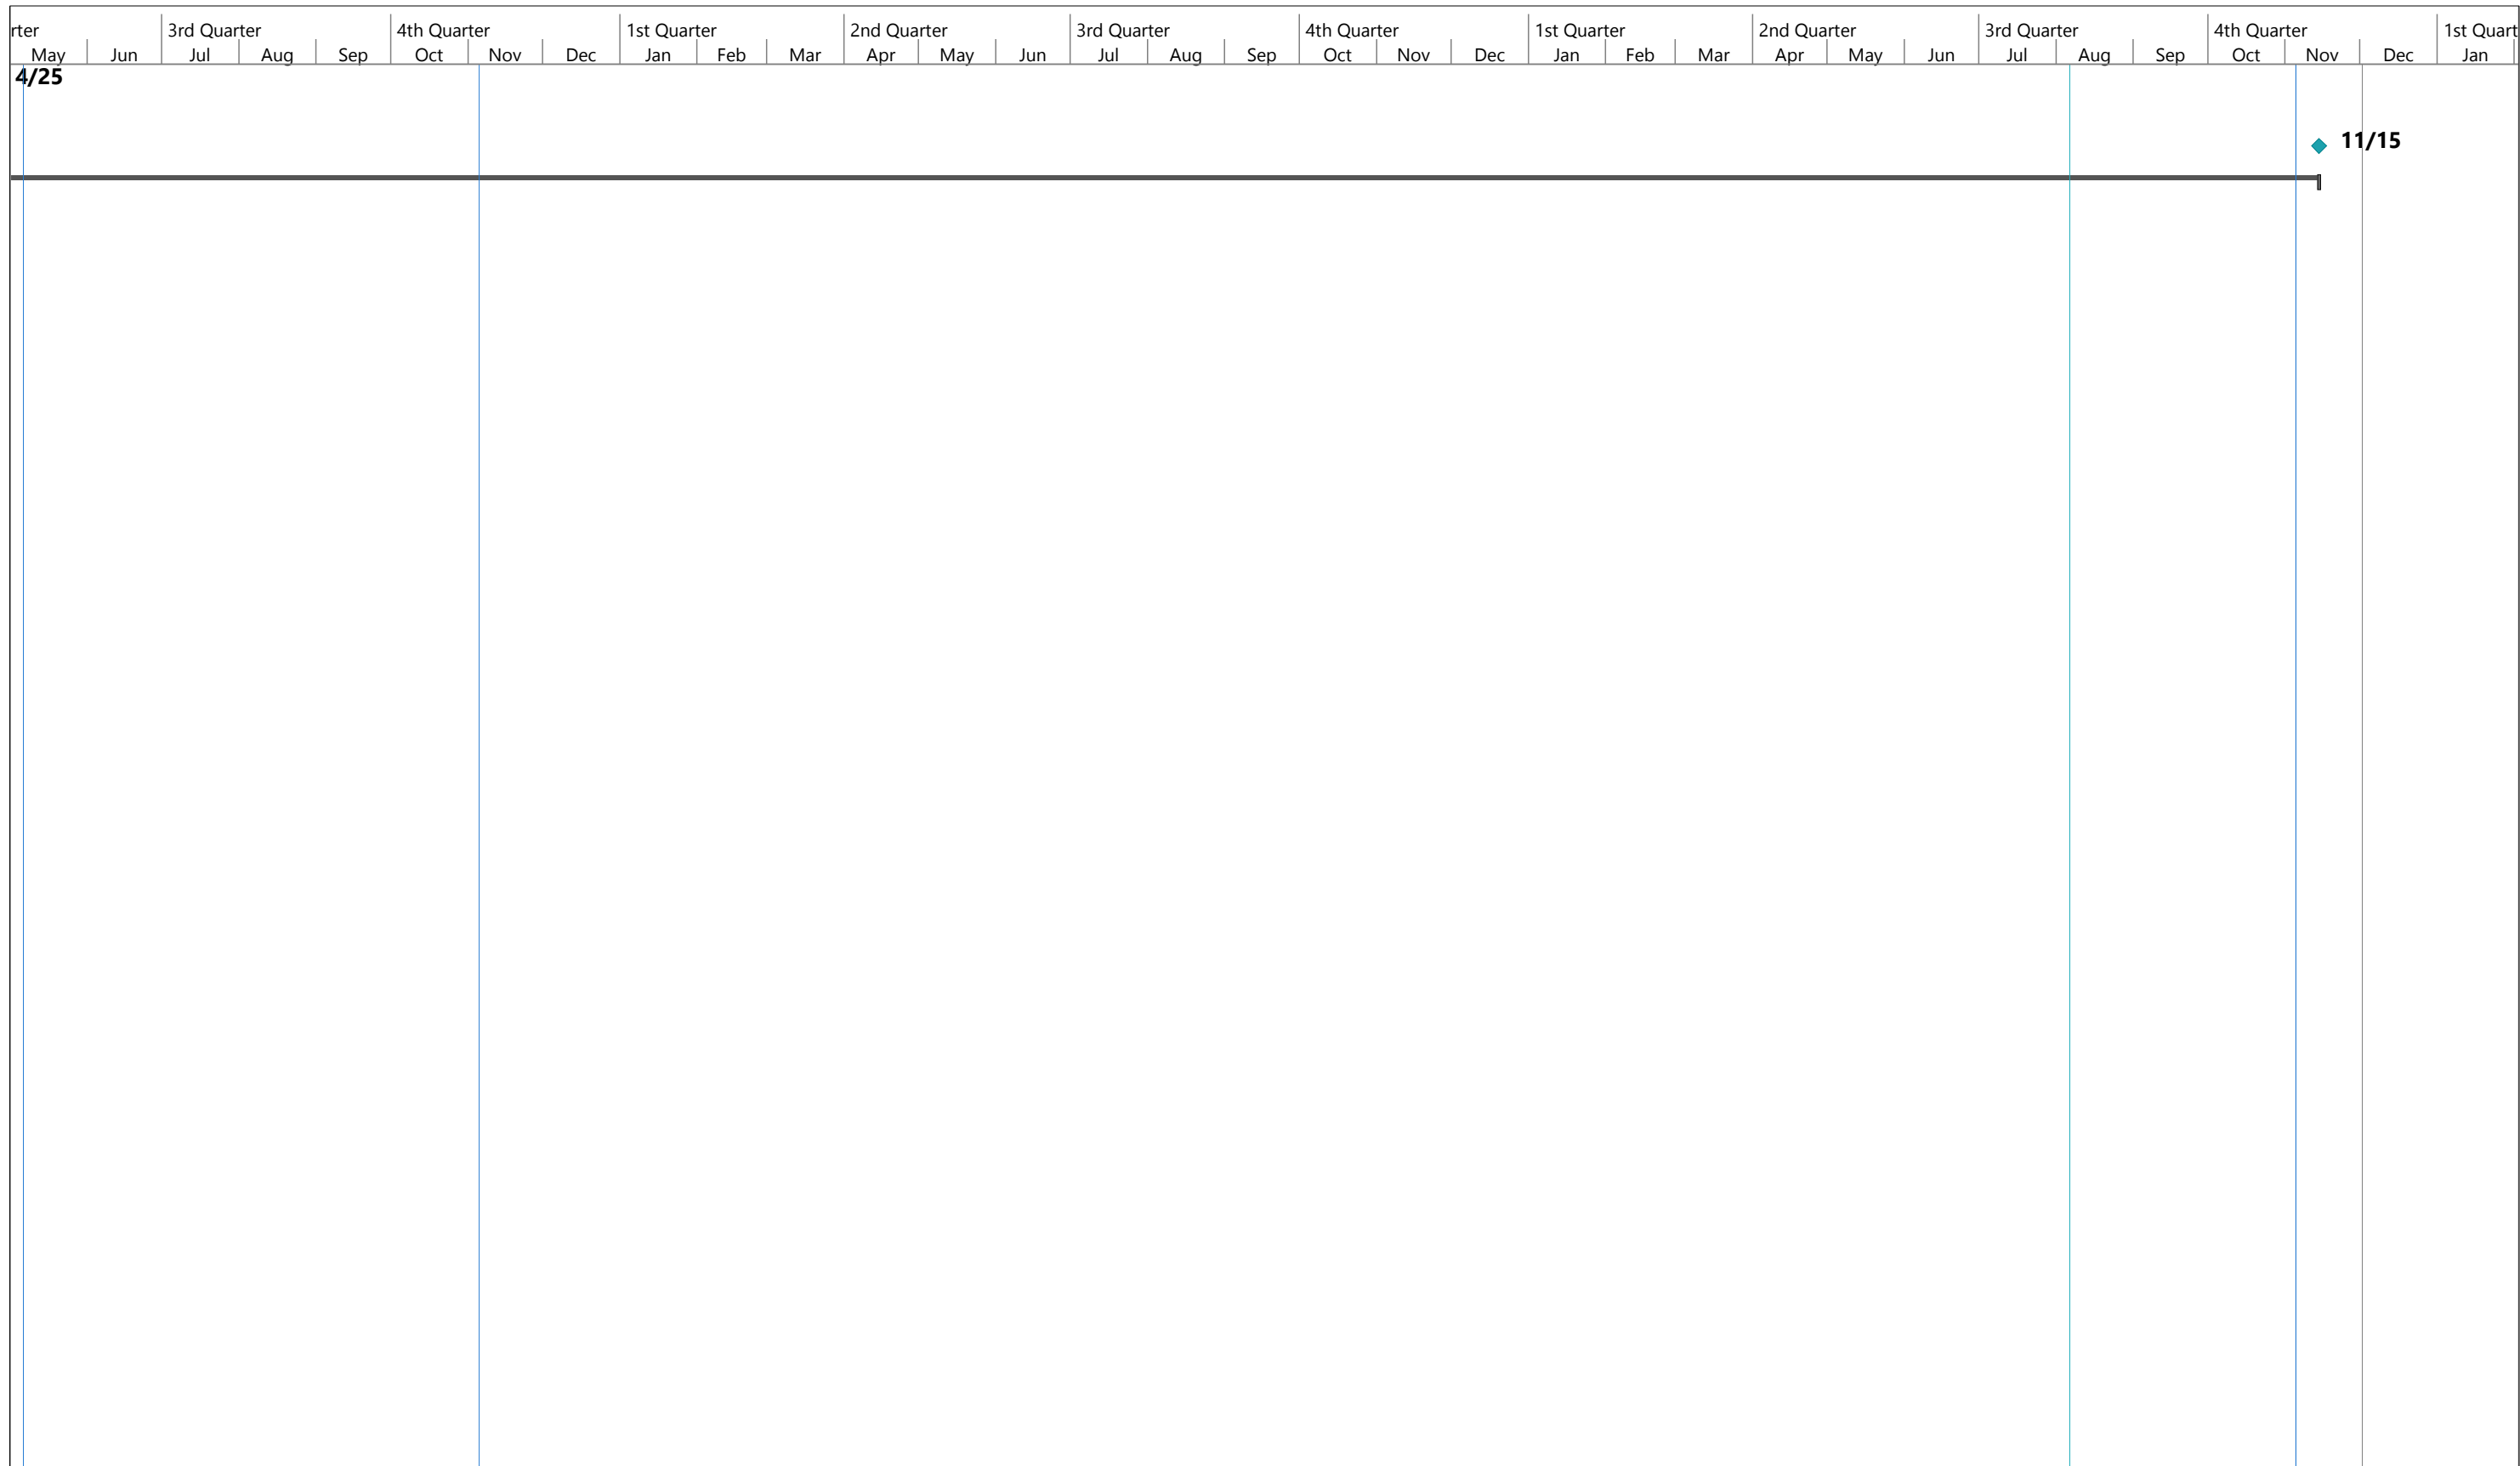


Project: Detail Implementation
Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

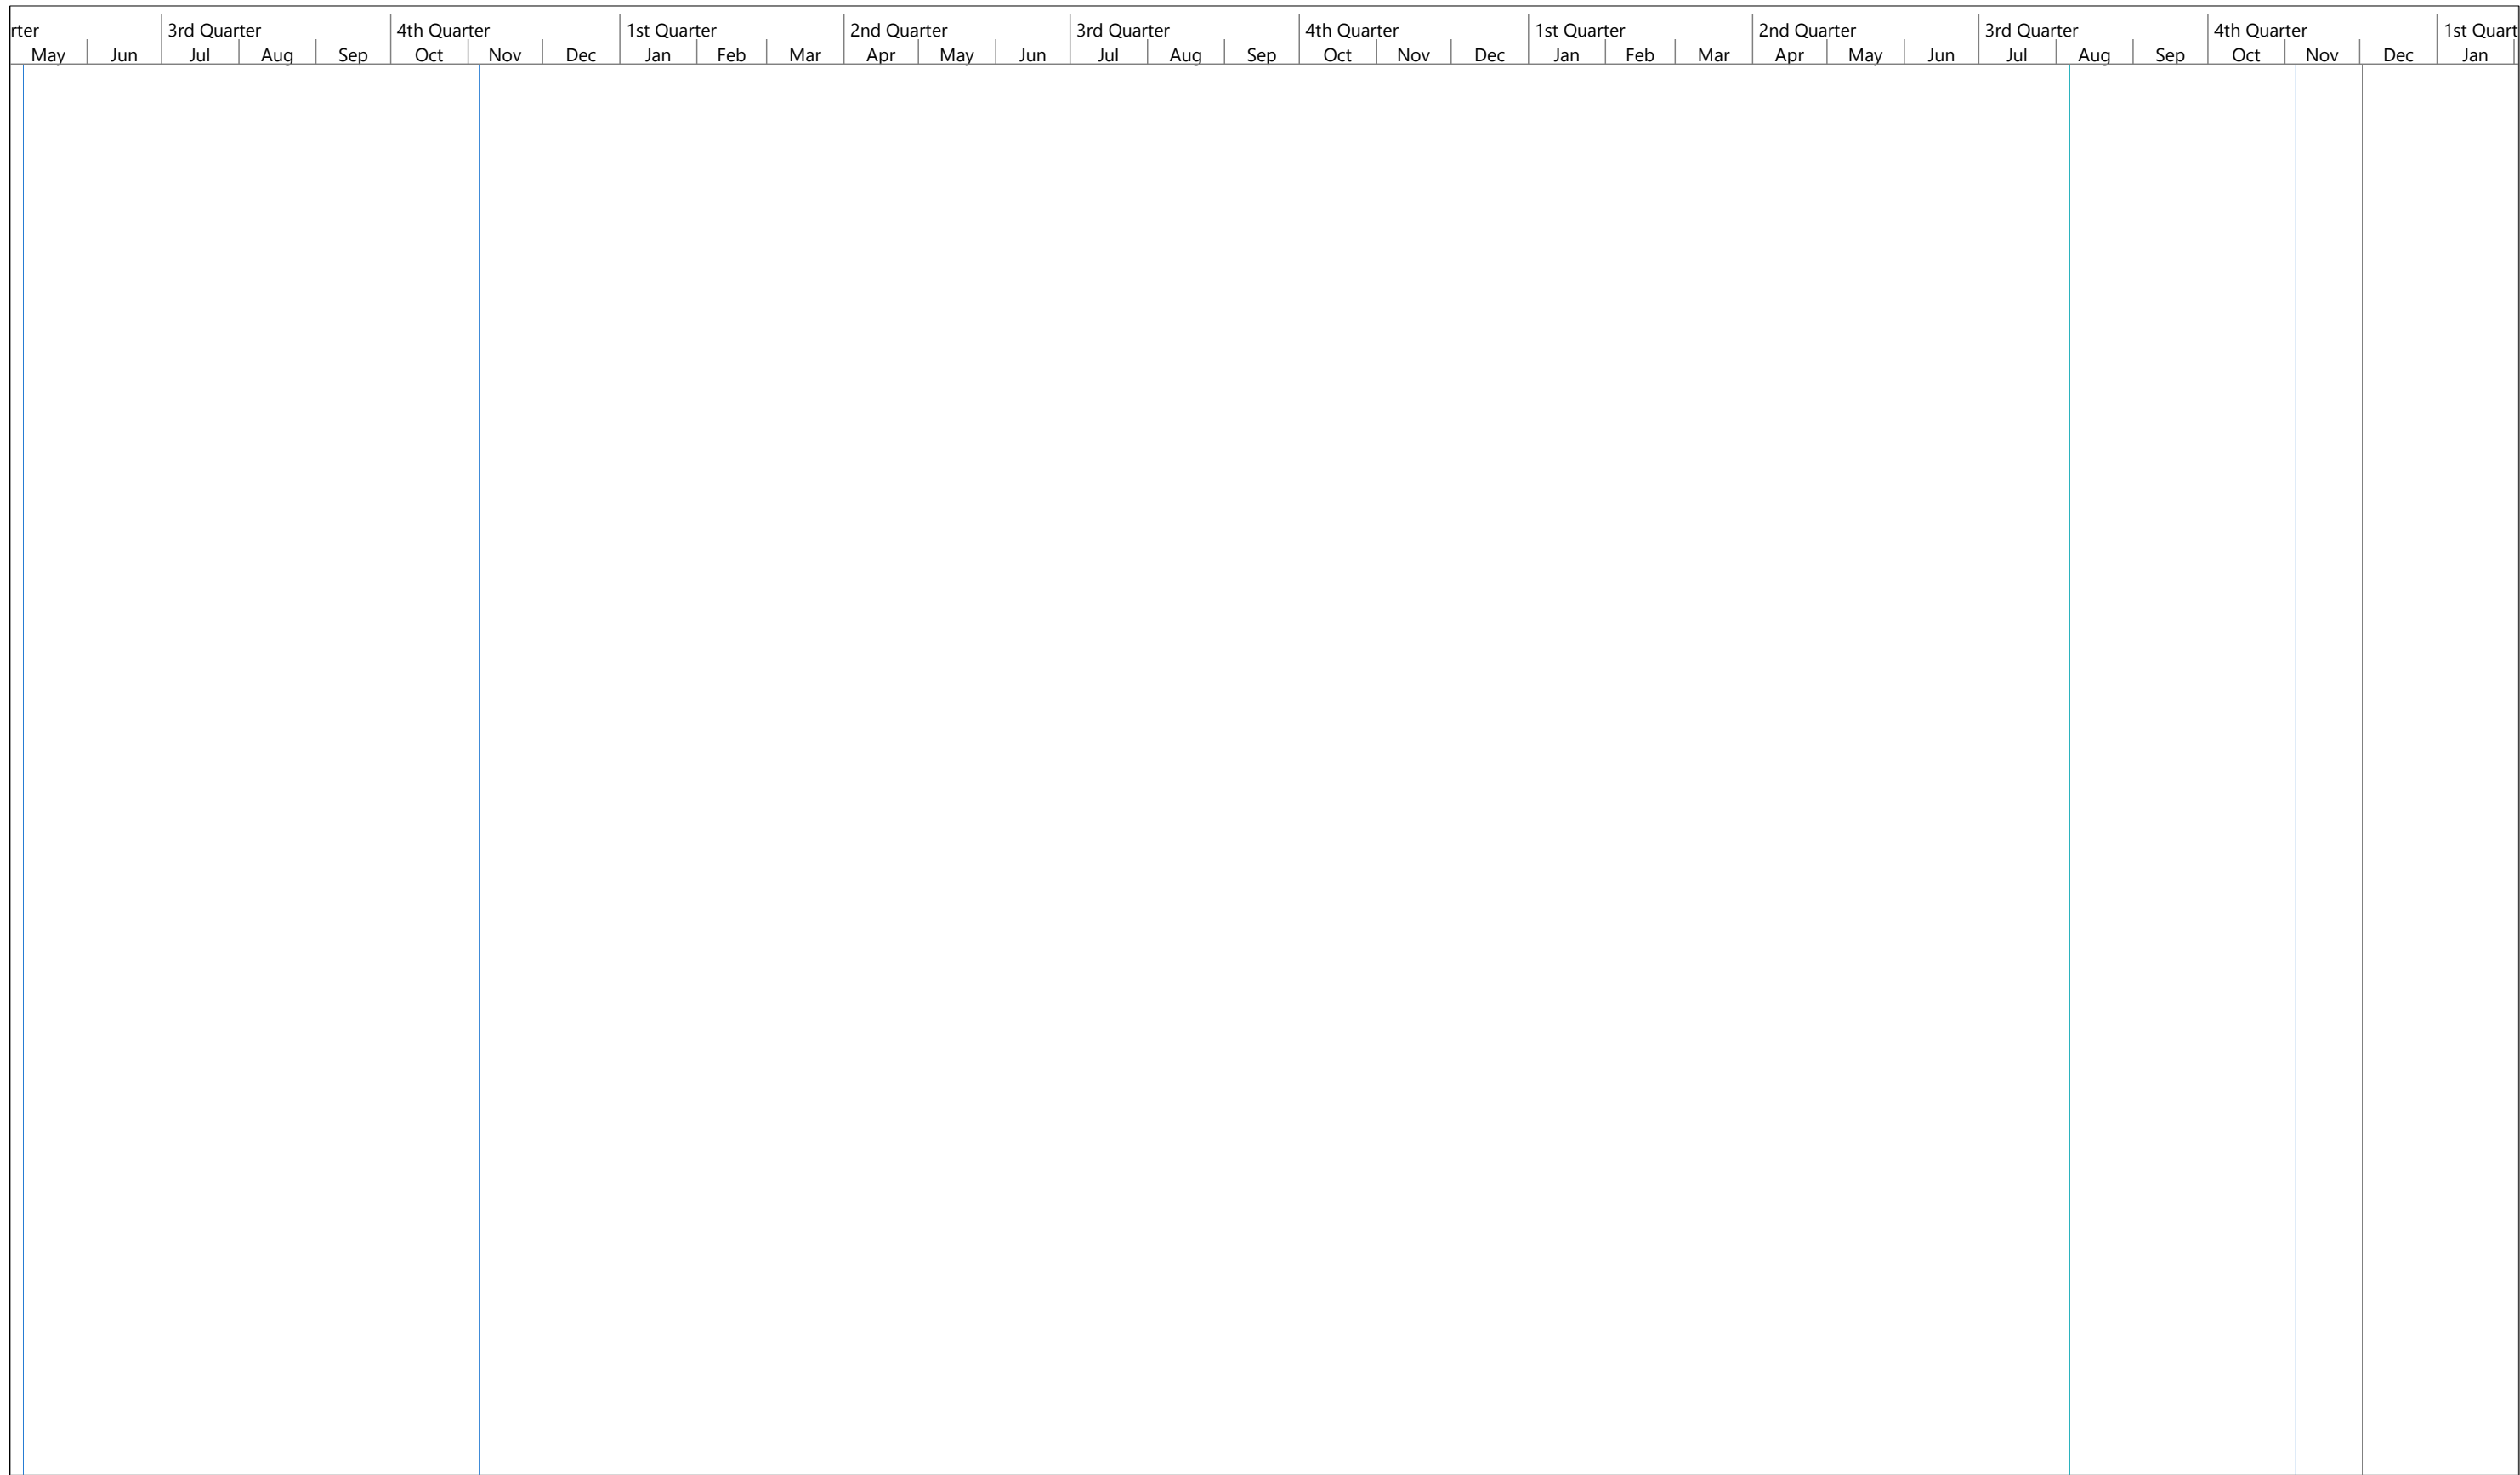


Project: Detail Implementation
Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

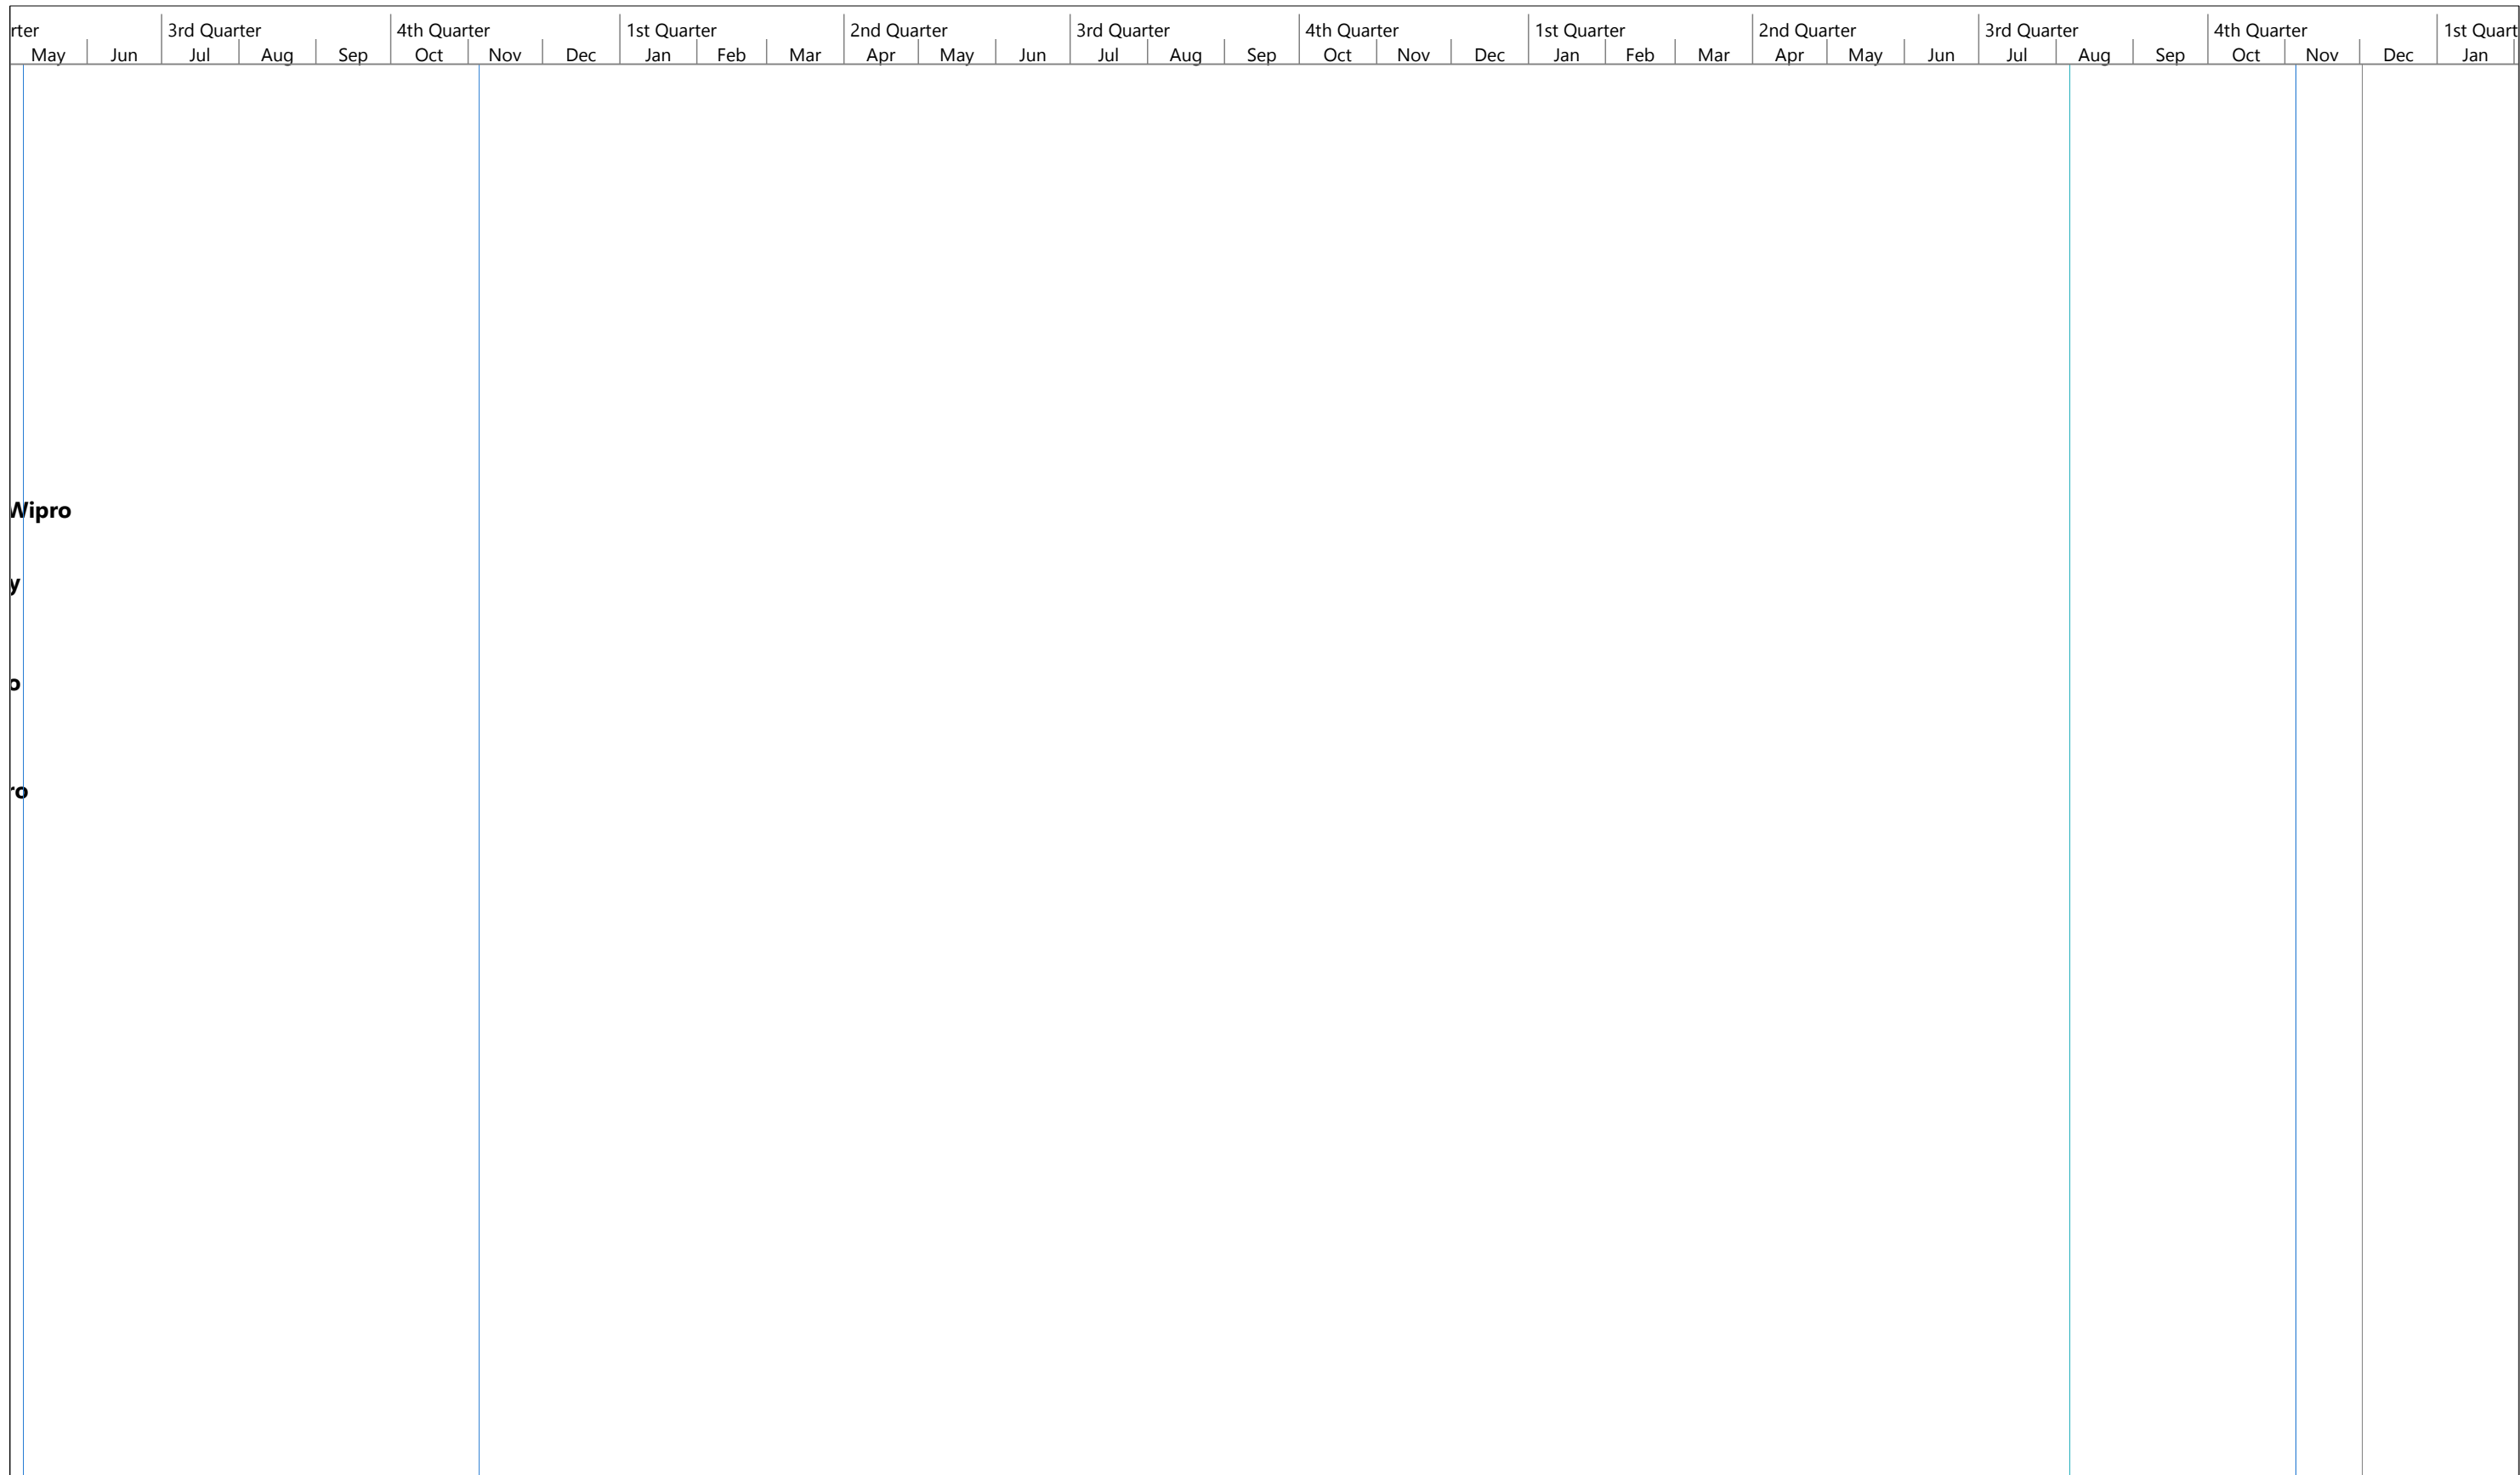


Project: Detail Implementation
Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

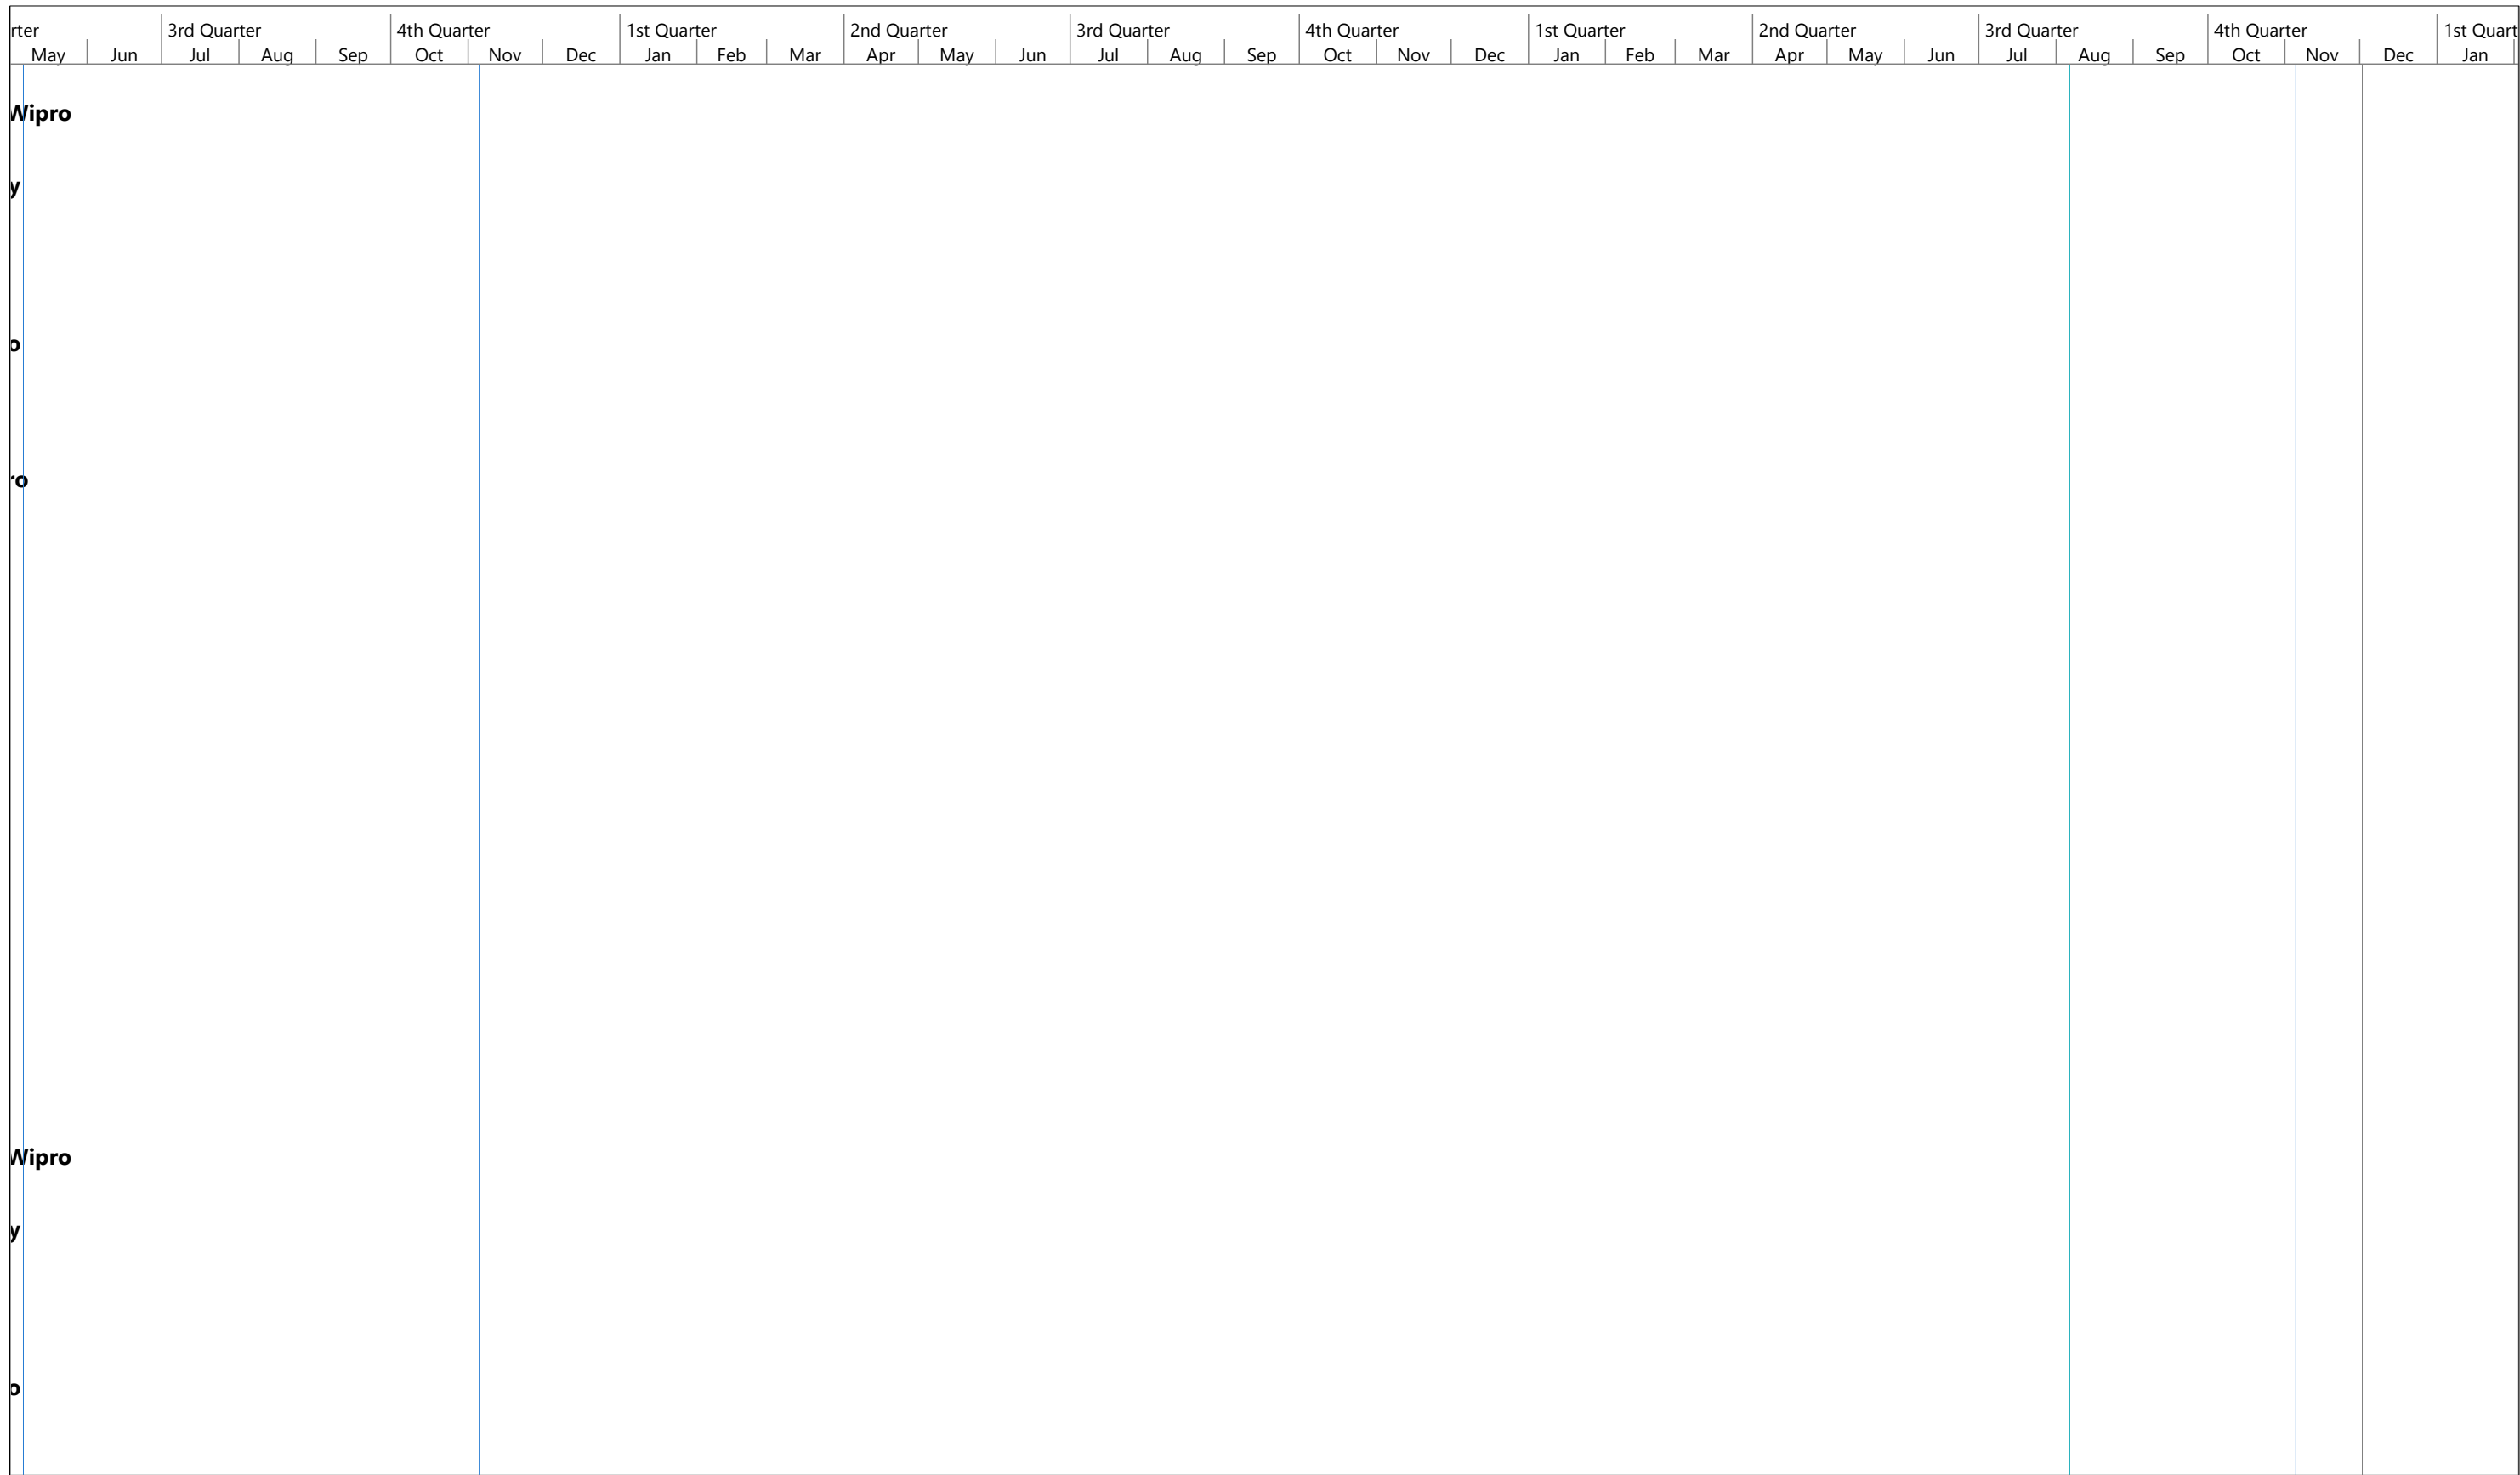


Project: Detail Implementation
Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

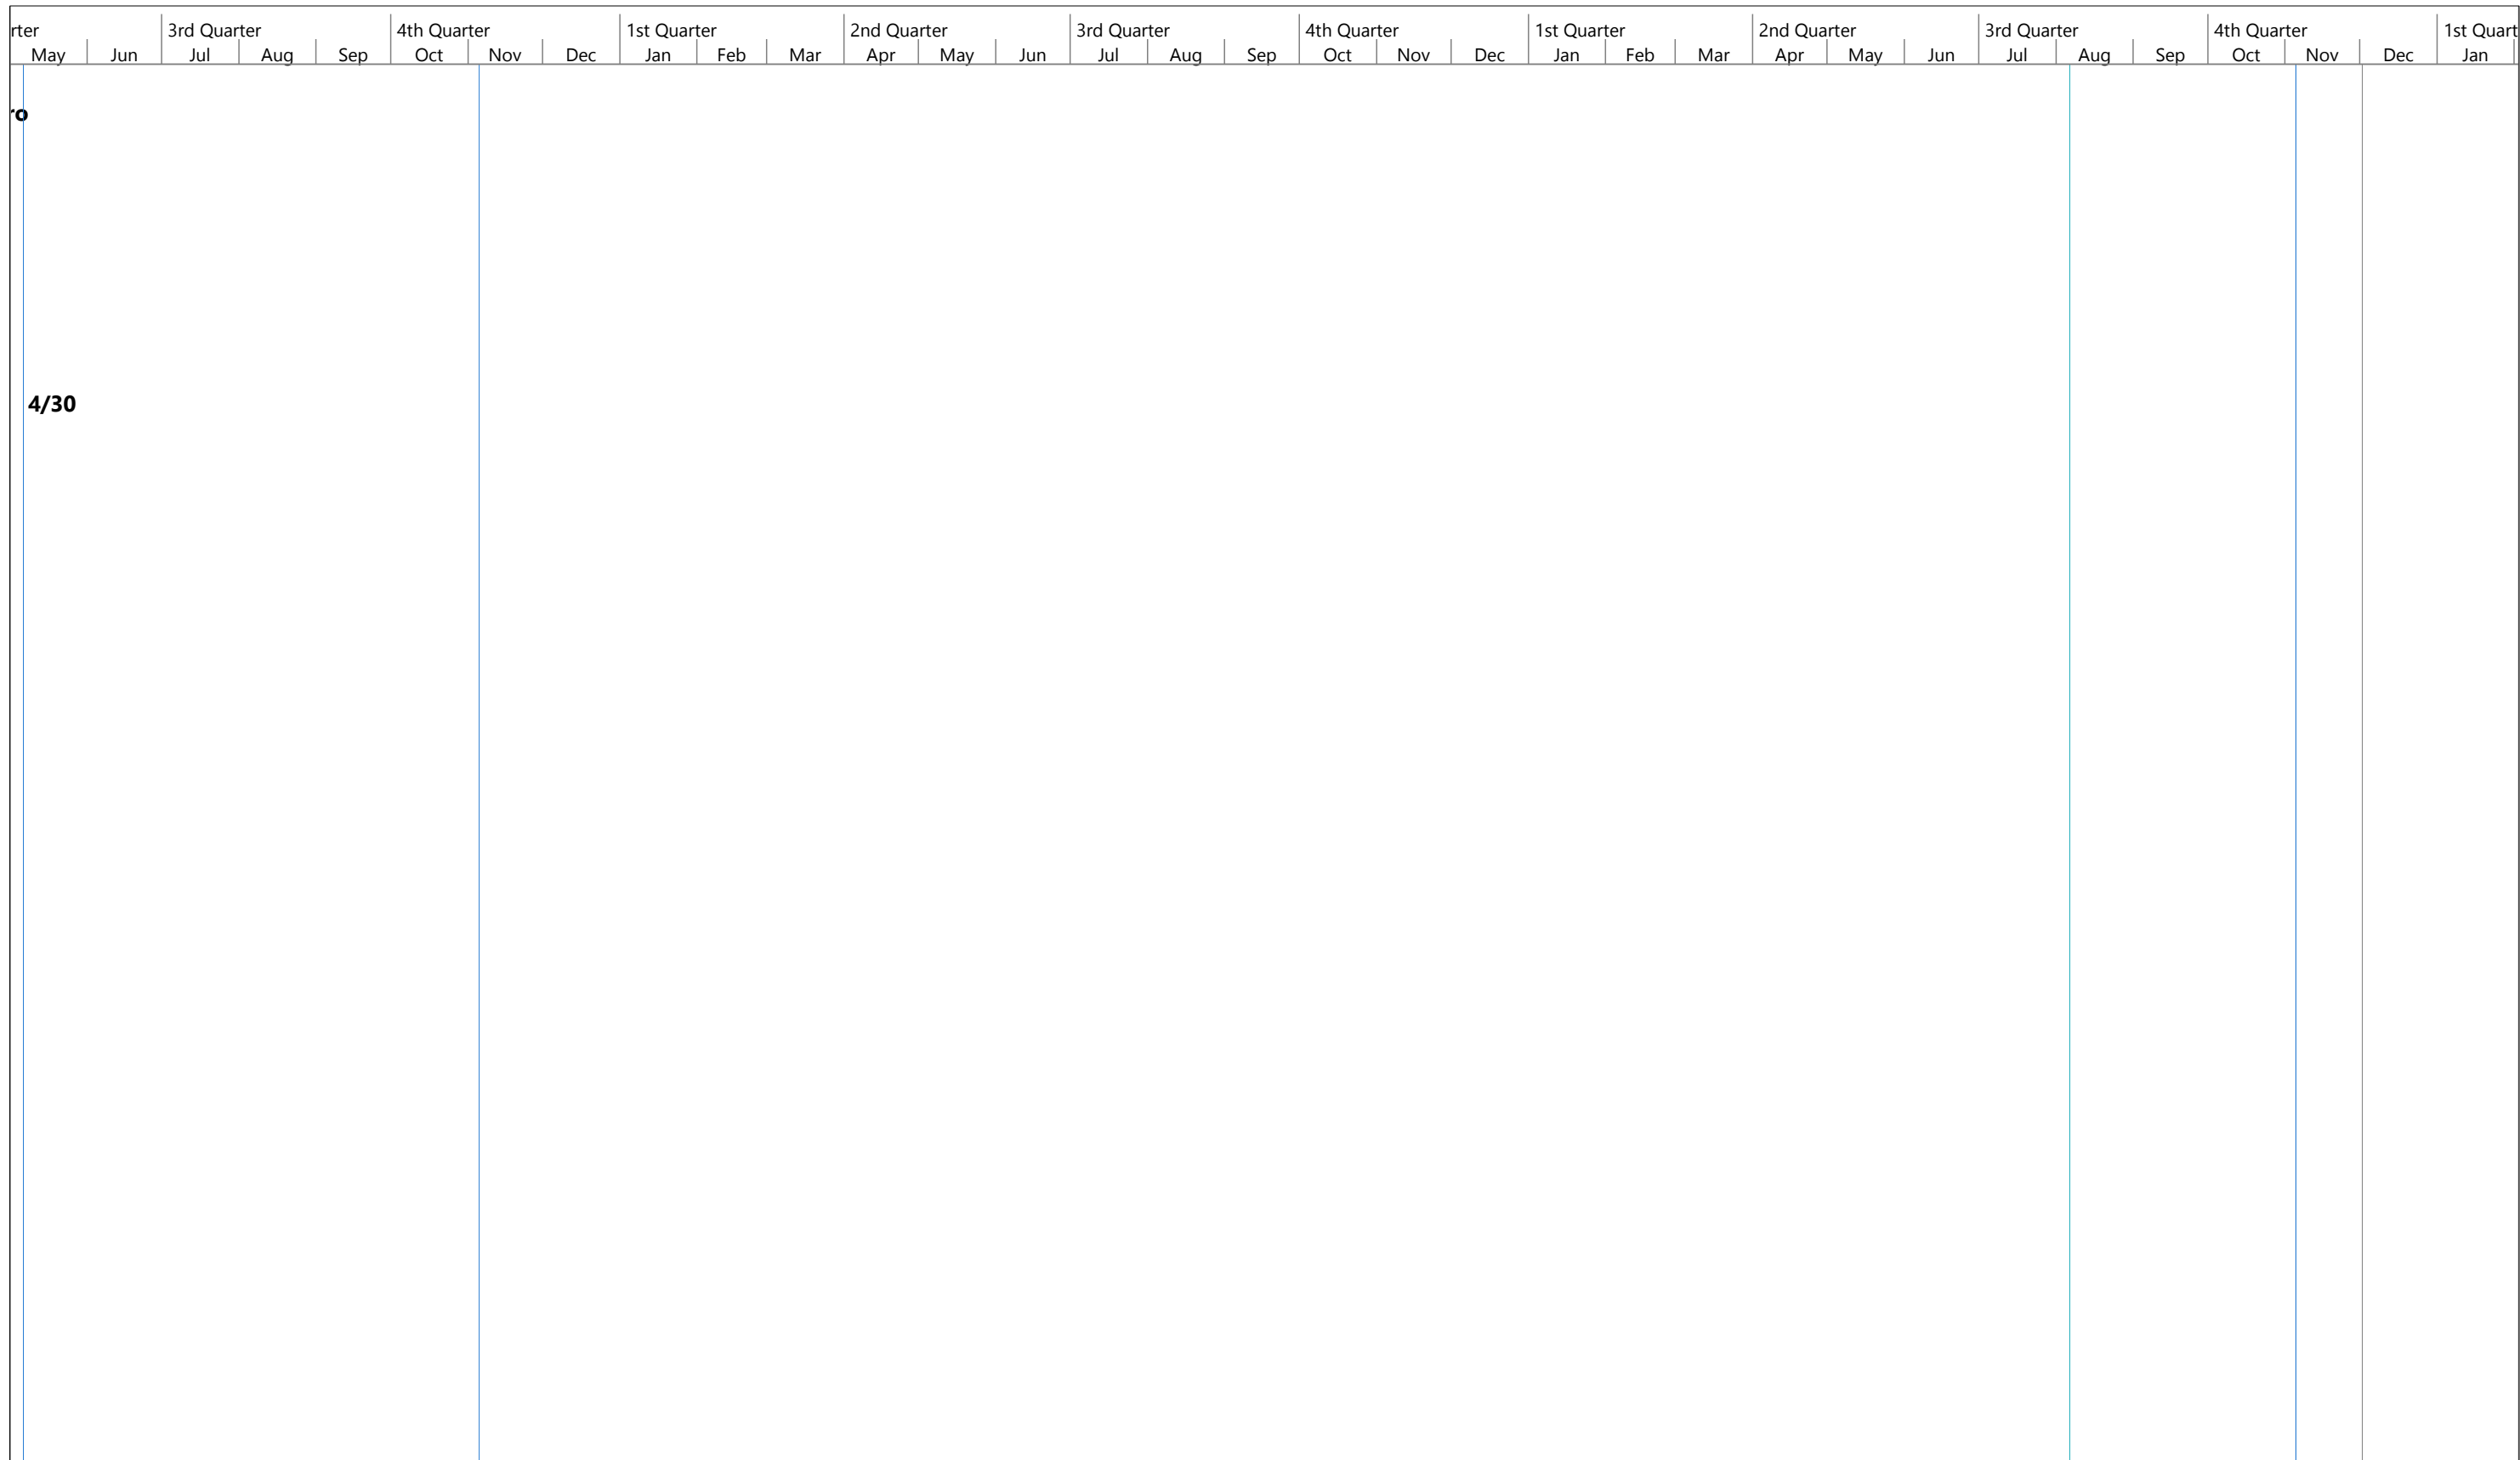

Project: Detail Implementation
Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

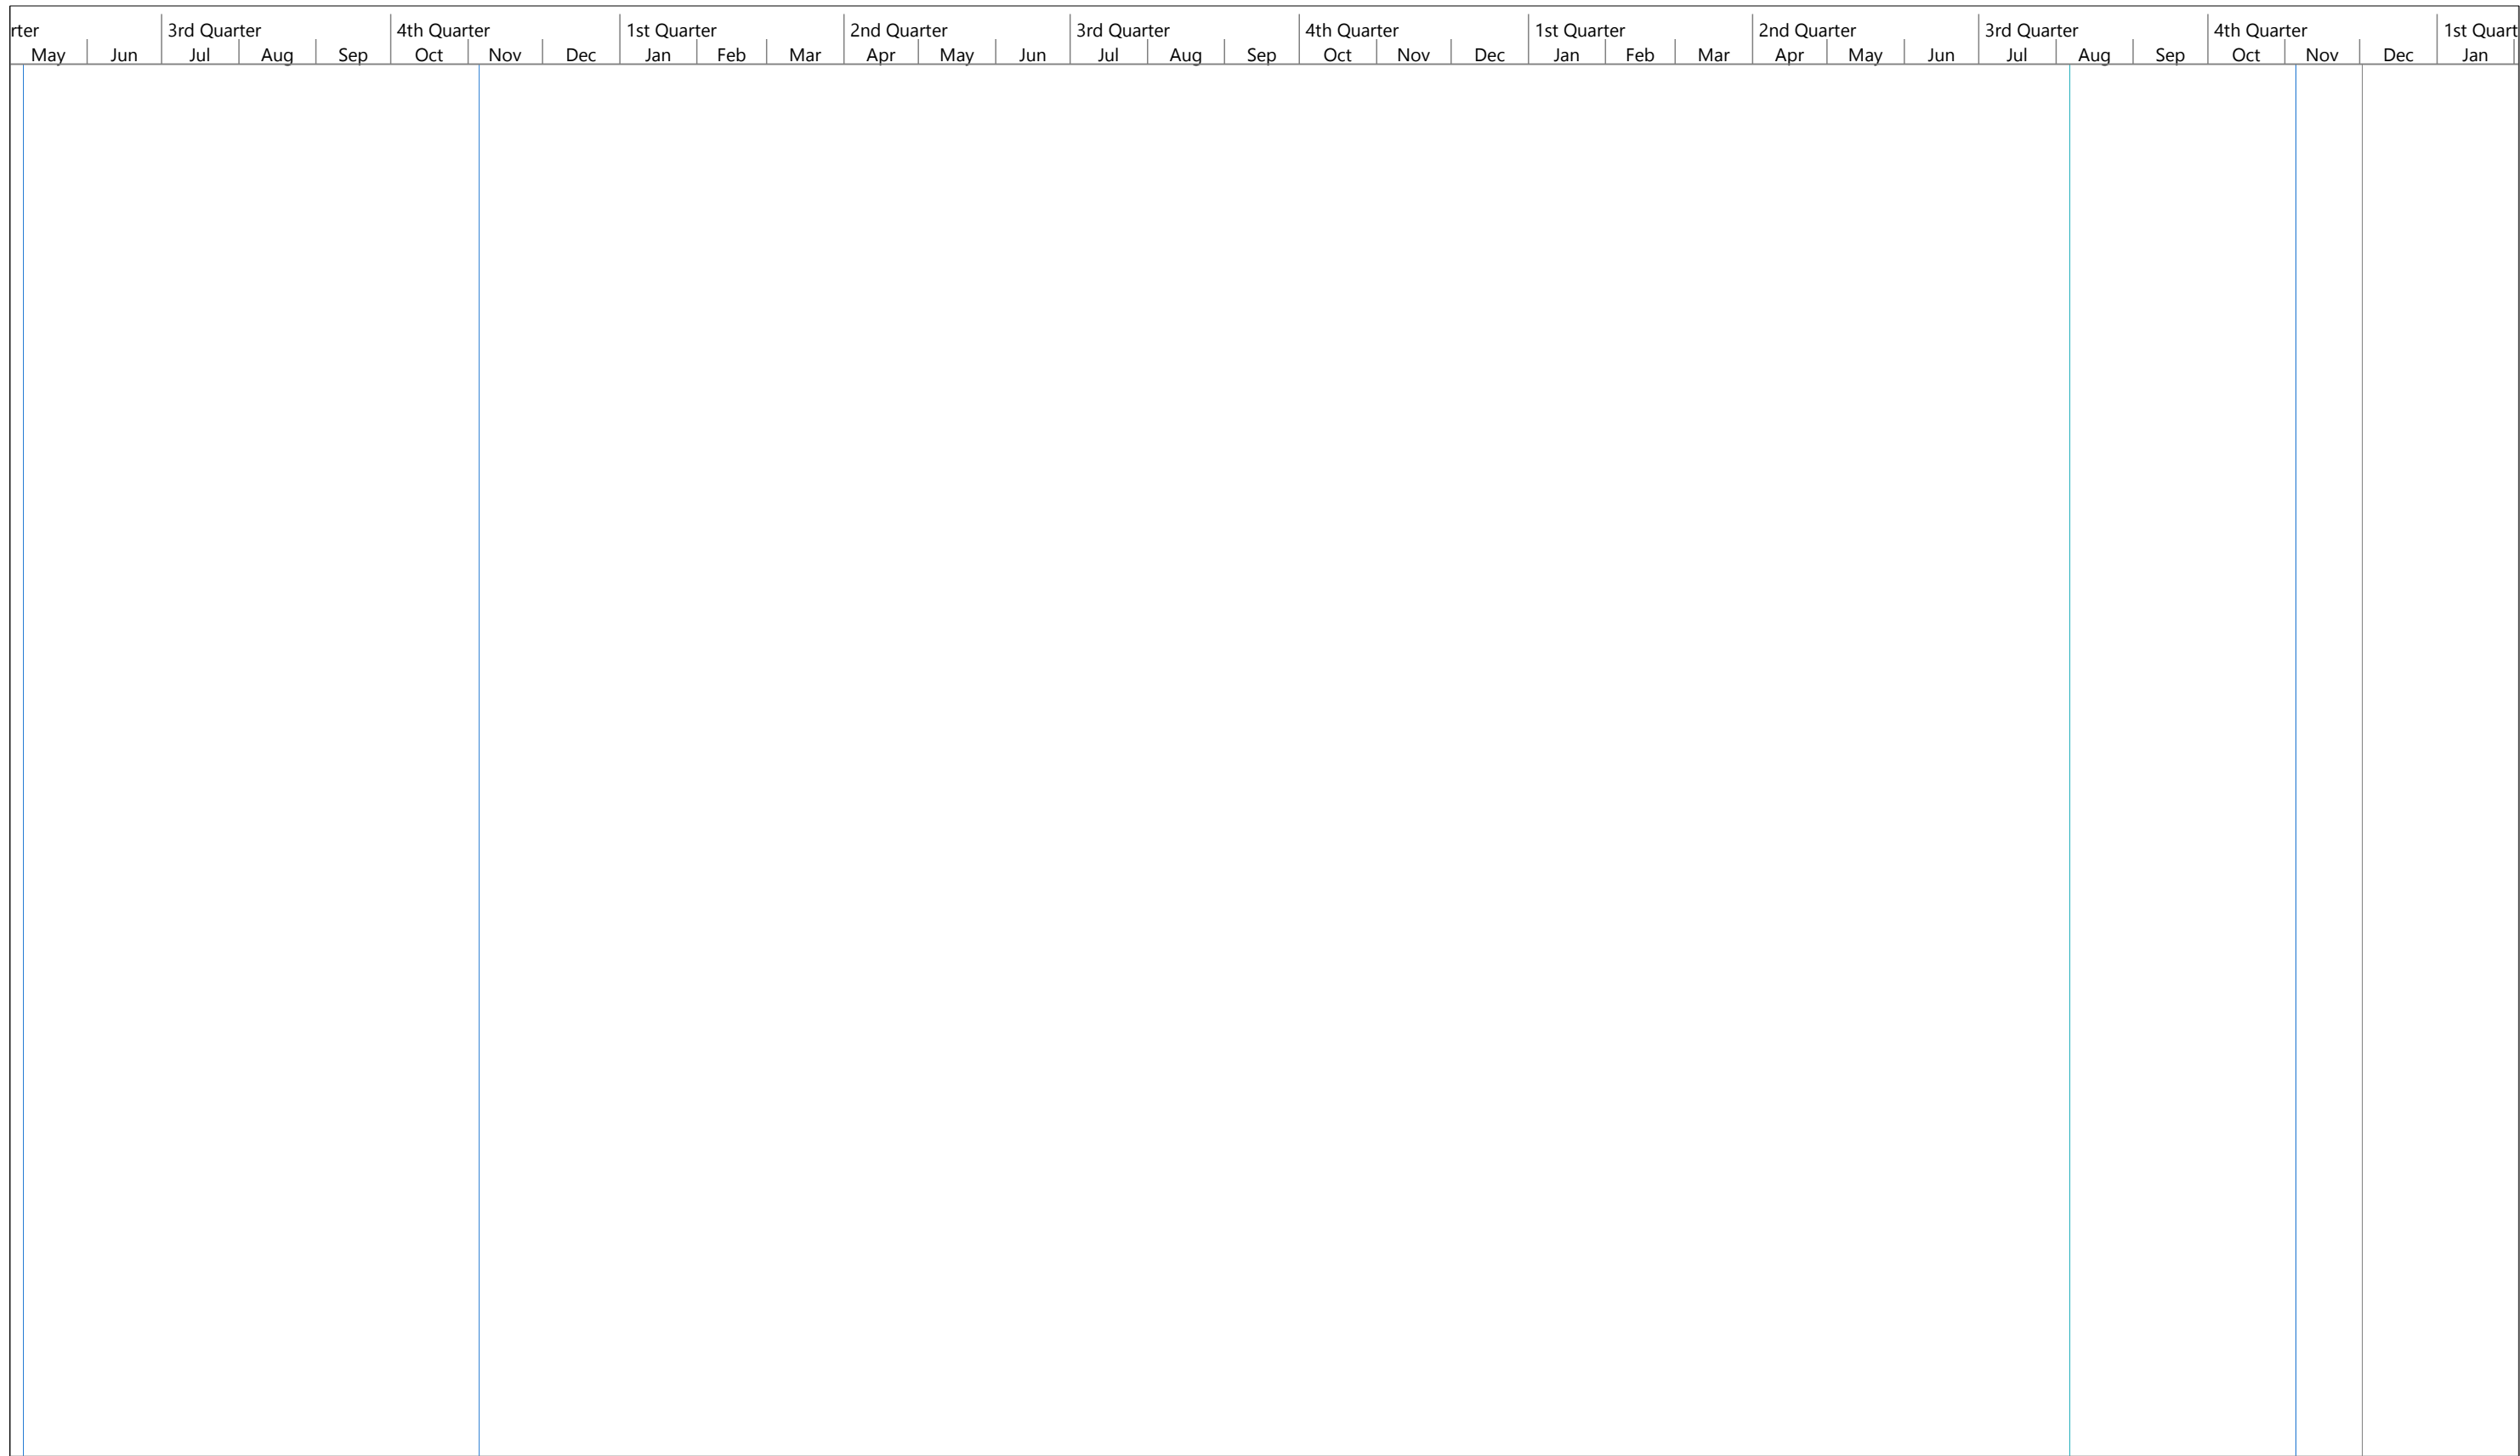

Project: Detail Implementation
Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			



Project: Detail Implementation
Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

ipro
ipro
ipro
ipro,Authority


Project: Detail Implementation
Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			



Project: Detail Implementation
Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

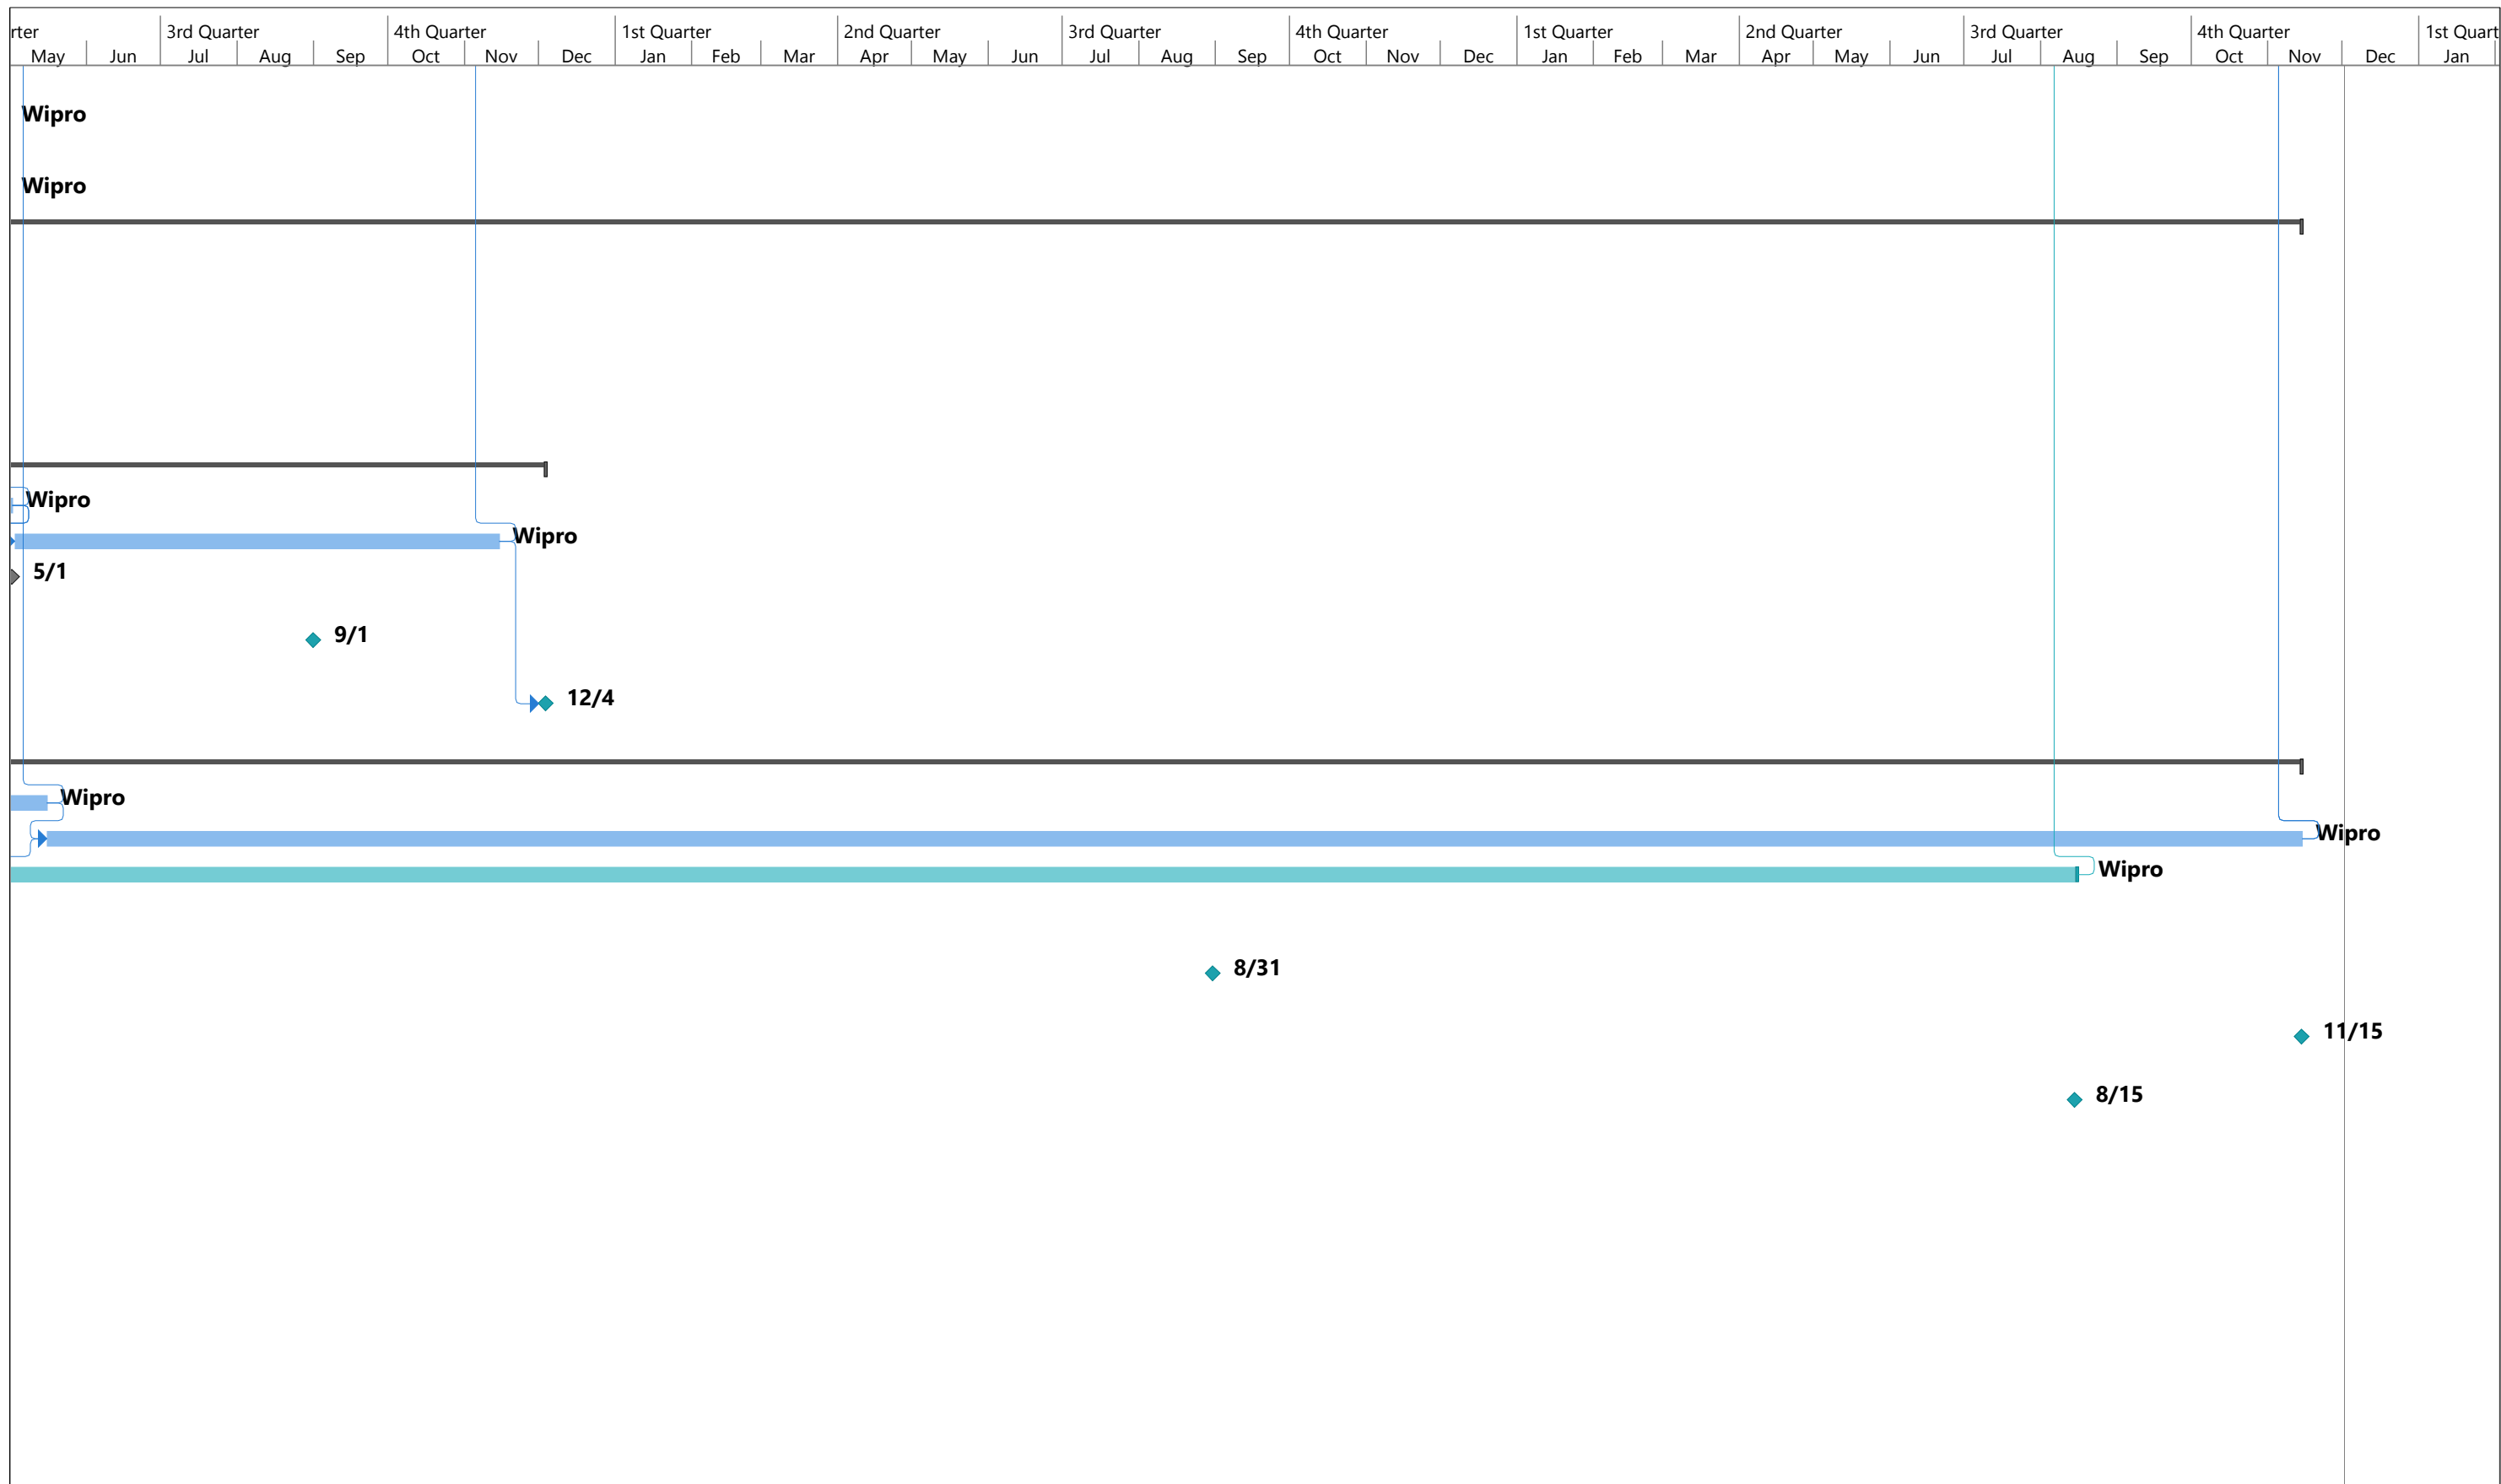

Project: Detail Implementation
Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			



◆ 12/1

Project: Detail Implementation
Date: Jun 5 '16

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			
