ID	Task Mode	Task Name	Duration	Start	Finish	Critical	Predecessors
1		**THC Integrated transition & Transformation Plan**	**859 days?**	**Aug 1 '16**	**Nov 15 '19**	**Yes**	
2		MS :Contract Sign off	1 day	Sep 6 '16	Sep 6 '16	No	
3		MS:Agreed Implementation Plan	0 days	Oct 4 '16	Oct 4 '16	No	35
4		MS: Network Migration Link Commissioning	0 days	Nov 16 '16	Nov 16 '16	No	31
5		MS: Service Desk, DC Infrastructure and tools Setup Complete	1 day	Dec 12 '16	Dec 12 '16	No	45,52
6		MS: Tranche 1 ATP Services Go Live (SD, EUC, App Ops)	0 days	Feb 17 '17	Feb 17 '17	No	39,40,41
7		MS: Tranche 2 ATP Services Go Live (DC Support)	0 days	Mar 10 '17	Mar 10 '17	No	42
8		MS:CPP Services Stabilized	0 days	May 1 '17	May 1 '17	No	39,40,41,42
9		MS ATP :Transformation Project 1- Active Directory (including processes for joiners/movers/leavers)	0 days	Feb 9 '17	Feb 9 '17	No	60
10		MS CPP Transformation Project 1- Active Directory (including processes for joiners/movers/leavers)	0 days	Mar 1 '17	Mar 1 '17	No	9
11		MS ATP Transformation Project 2 - Data Centre Transformation	0 days	Mar 10 '17	Mar 10 '17	No	55
12		MS Transformation Project 2 - DC Setup Complete and Microsoft Office Milestone	1 day	Dec 13 '16	Dec 13 '16	No	52
13		MS CPP Transformation Project 2 - Data Centre Transformation	0 days	Apr 1 '17	Apr 1 '17	No	11
14		MS Key Core Services Transition Completed and Transformation Projects 1, 2 & 6 Complete	0 days	Apr 1 '17	Apr 1 '17	No	13
15		MS CPP Transformation Project Office Replacement Service	1 day?	Jun 6 '17	Jun 6 '17	No	61
16		MS ATP Transformation Project 3 - Corporate Desktop Refresh	0 days	May 1 '17	May 1 '17	No	69FS+30 days
17		MS Key Transformation Project 3 – Corporate Desktop Refresh	0 days	Sep 1 '17	Sep 1 '17	No	16
18		MS CPP Transformation Project 3 - Corporate Desktop Refresh	0 days	Nov 15 '17	Nov 15 '17	No	70
19		MS ATP Transformation Project 4 - Curriculum Desktop Refresh	0 days	May 15 '17	May 15 '17	No	72SS
20		MS CPP Transformation Project 4 - Curriculum Desktop Refresh	0 days	Nov 15 '19	Nov 15 '19	Yes	72
21		MS ATP LMD - Deployment and final removal of devices	0 days	Aug 16 '19	Aug 16 '19	No	71
22		MS Transformation Project 3 and 4 – Desktop Environment Setup Complete	0 days	Nov 15 '19	Nov 15 '19	Yes	70,72
23		MS CPP Transformation Project 5 – Business Application transformation	0 days	Feb 16 '17	Feb 16 '17	No	73
24		MS CPP Transformation Project 6 – Key applications Self Service	0 days	Apr 25 '17	Apr 25 '17	No	67
25		MS All Transition and Transformation Projects Completed	0 days	Nov 15 '19	Nov 15 '19	Yes	
26		**Transition & Transformation Programme**	**859 days**	**Aug 1 '16**	**Nov 14 '19**	**Yes**	
27		LOI Release	1 day	Aug 25 '16	Aug 25 '16	No	
28		**Transition**	**177 days**	**Aug 25 '16**	**Apr 28 '17**	**Yes**	
29		**Transition Enablement**	**141 days**	**Aug 25 '16**	**Mar 9 '17**	**No**	
30		**Infrastructure Set Up**	**100 days**	**Aug 25 '16**	**Jan 11 '17**	**No**	
31		Network Connectivity Set up	**60 days**	**Aug 25 '16**	**Nov 16 '16**	No	
32		Delivery Center Set Up	**85 days**	**Sep 15 '16**	**Jan 11 '17**	No	
33		Security Accreditation	133 days	**Sep 6 '16**	**Mar 9 '17**	No	
34		**Transition Governance**	**20 days**	**Sep 7 '16**	**Oct 4 '16**	**No**	
35		Transition Planning	**20 days**	**Sep 7 '16**	**Oct 4 '16**	No	
36		HR Transition	**115 days**	**Sep 6 '16**	**Feb 13 '17**	No	
37		Contract Novation	**90 days**	**Oct 17 '16**	**Feb 17 '17**	No	
38		**Knowledge Transition**	**89 days**	**Nov 8 '16**	**Mar 10 '17**	**No**	
39		Service Desk Tower	**73 days**	**Nov 8 '16**	**Feb 16 '17**	No	
40		Field and Deskside Support	**73 days**	**Nov 8 '16**	**Feb 16 '17**	No	
41		Application Support Transition	**73 days**	**Nov 8 '16**	**Feb 16 '17**	No	
42		DC Services Learning(Internal)	**40 days**	**Jan 16 '17**	**Mar 10 '17**	No	
43		**Process & Tools Transition**	**79 days**	**Sep 6 '16**	**Dec 23 '16**	**No**	
44		Assessment & Design	**30 days**	**Sep 6 '16**	**Oct 17 '16**	No	
45		Align & Implement	**30 days**	**Oct 18 '16**	**Nov 28 '16**	No	
46		Training and On-boarding	**20 days**	**Nov 28 '16**	**Dec 23 '16**	No	
47		Tools Implementation & Automation	115 days	Aug 25 '16	Feb 1 '17	No	
48		**TP2: Data Center Transformation**	**179 days**	**Aug 4 '16**	**Apr 11 '17**	**No**	
49		Program Initiation & Planning Stage	**74 days**	**Aug 4 '16**	**Nov 15 '16**	No	
50		Discovery and Assessment	**15 days**	**Oct 4 '16**	**Oct 24 '16**	No	
51		Planning and Design- Implementation	**20 days**	**Oct 18 '16**	**Nov 14 '16**	No	
52		**Planning and Design- Transformation**	**30 days**	**Nov 1 '16**	**Dec 12 '16**	No	
53		**Systems Deployment and Integration**	**30 days**	**Oct 18 '16**	**Nov 28 '16**	No	
54		Transformation Preparation	**90 days**	**Oct 4 '16**	**Feb 6 '17**	No	
55		Transformation Execution (Recursive) From Fujitsu DC	**87 days**	**Nov 9 '16**	**Mar 9 '17**	No	
56		**Training and Handover**	**110 days**	**Nov 9 '16**	**Apr 11 '17**	No	
57		**TP1:Active Directory Transformation**	**116 days**	**Aug 31 '16**	**Feb 8 '17**	**No**	
58		Active Directory Infrastructure	**65 days**	**Sep 20 '16**	**Dec 19 '16**	No	
59		Active Directory Logical Structure for JML	**55 days**	**Oct 18 '16**	**Jan 2 '17**	No	
60		Azure AD Integration	**116 days**	**Aug 31 '16**	**Feb 8 '17**	No	
61		TP3A&TP4A:Replacement Office Service(O365 Implementation)	113 days	Oct 18 '16	Mar 23 '17	No	
62		Desktop Application Packaging	120 days	Oct 4 '16	Mar 20 '17	No	
63		**TP6: Store & TP3/4 Enablement Activities :LiVE Workspace Implementation including VirtuaDesk, Workspace Mgmt, InTune and JML Automation**	**135 days**	**Oct 18 '16**	**Apr 24 '17**	**No**	
64		Planning and Design	40 days	Oct 18 '16	Dec 12 '16	No	
65		Build and Testing	72 days	Nov 29 '16	Mar 8 '17	No	
66		Deployment/Migration	40 days	Feb 28 '17	Apr 24 '17	No	
67		Enhance	60 days	Jan 31 '17	Apr 24 '17	No	
68		**TP3B&TP4B: EUD Refresh Planning and Rollout**	**833 days**	**Sep 6 '16**	**Nov 14 '19**	**Yes**	
69		Migration Planning Toolset	140 days	Sep 6 '16	Mar 20 '17	No	
70		TP3B: Corporate EUD Refresh Rollout	171 days	Mar 21 '17	Nov 14 '17	No	
71		LMD Deployment Coordination	648 days	Feb 21 '17	Aug 15 '19	No	
72		TP4B: Curriculum EUC Refresh	717 days	Feb 15 '17	Nov 14 '19	Yes	
73		TP5: Application Rationalization Assessment	143 days	Aug 1 '16	Feb 15 '17	No	

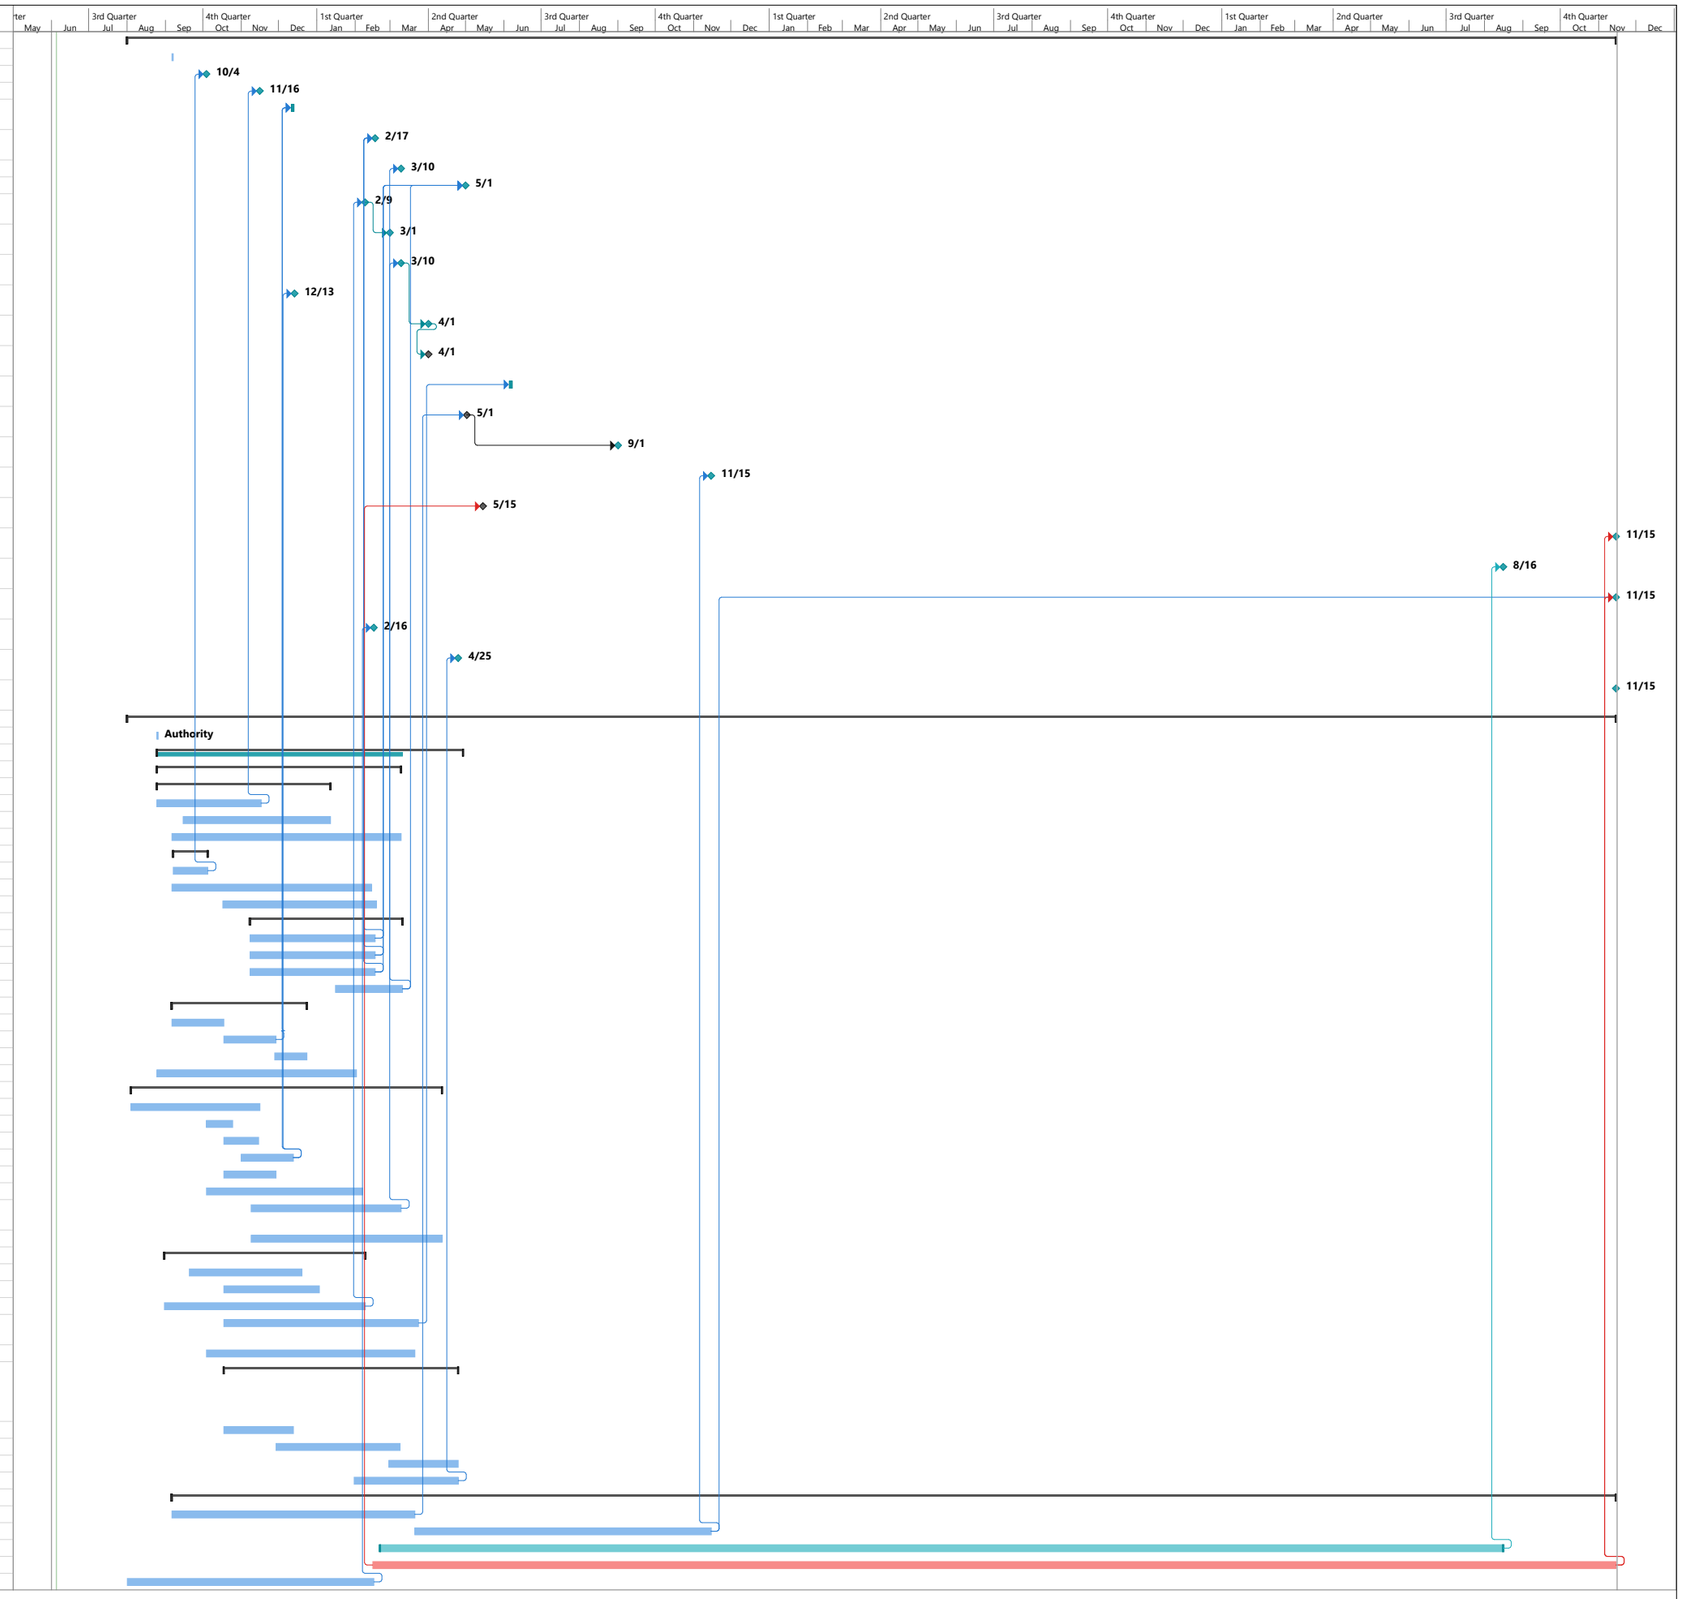

Project: Integrated Transition an
Date: Jun 5 '16

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress
